







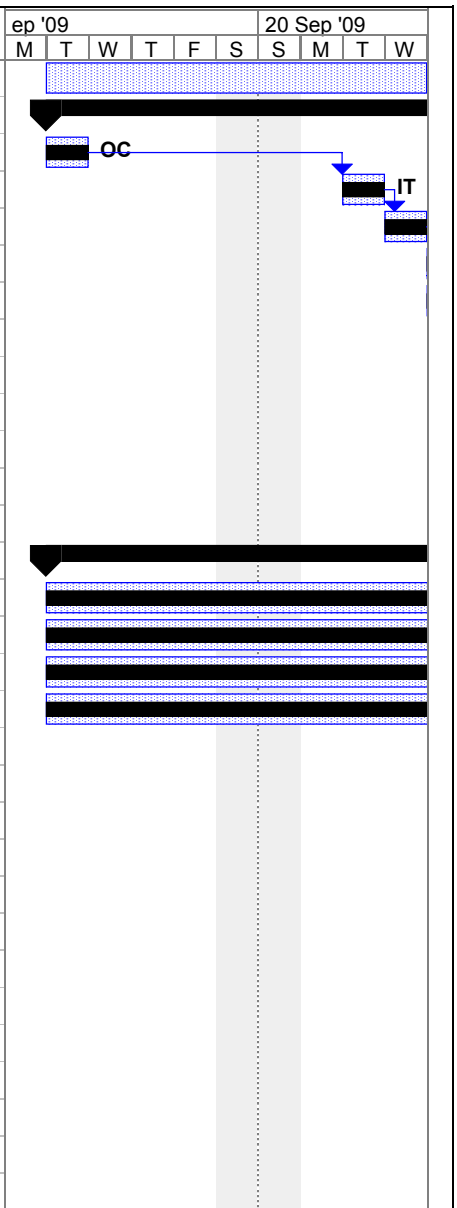



ID	Task Name	Duration	Start	Finish	Predecessors	ep '09							20 Sep '09						
						M	T	W	T	F	S	S	M	T	W				
1	<b>Equipment</b>	7 days	Tue 15/09/09	Wed 23/09/09															
2	<input checked="" type="checkbox"/> <b>Test Server</b>	<b>8 days</b>	<b>Tue 15/09/09</b>	<b>Thu 24/09/09</b>															
3	<input checked="" type="checkbox"/> Test Server Delivery	1 day	Tue 15/09/09	Tue 15/09/09															
4	<input checked="" type="checkbox"/> Test Server Racked	1 day	Tue 22/09/09	Tue 22/09/09	3														
5	<input checked="" type="checkbox"/> Test Server configured on the network	1 day	Wed 23/09/09	Wed 23/09/09	4														
6	<input checked="" type="checkbox"/> Omnicell Remote access granted	1 day	Thu 24/09/09	Thu 24/09/09	5														
7	<input checked="" type="checkbox"/> OCRA connections created from Pharmacy	1 day	Thu 24/09/09	Thu 24/09/09	5														
8	<input checked="" type="checkbox"/> <b>Production Server</b>	<b>4 days</b>	<b>Mon 22/02/10</b>	<b>Thu 25/02/10</b>															
9	<input checked="" type="checkbox"/> Server Delivery	1 day	Mon 22/02/10	Mon 22/02/10															
10	<input checked="" type="checkbox"/> Server Racked	1 day	Tue 23/02/10	Tue 23/02/10	9														
11	<input checked="" type="checkbox"/> Server configured on the network	1 day	Wed 24/02/10	Wed 24/02/10	10														
12	<input checked="" type="checkbox"/> Omnicell Remote access granted	1 day	Thu 25/02/10	Thu 25/02/10	11														
13	<input checked="" type="checkbox"/> OCRA connections created from Pharmacy	1 day	Thu 25/02/10	Thu 25/02/10															
14	<input checked="" type="checkbox"/> <b>Software</b>	<b>56 days</b>	<b>Tue 15/09/09</b>	<b>Tue 01/12/09</b>															
15	<input checked="" type="checkbox"/> OCRA License	56 days	Tue 15/09/09	Tue 01/12/09															
16	<input checked="" type="checkbox"/> Allergy Alerts License	56 days	Tue 15/09/09	Tue 01/12/09															
17	<input checked="" type="checkbox"/> Clinical Pharmacology License	56 days	Tue 15/09/09	Tue 01/12/09															
18	<input checked="" type="checkbox"/> Web Browser License	56 days	Tue 15/09/09	Tue 01/12/09															
19	<input checked="" type="checkbox"/> <b>Pharmacy Interfaces</b>	<b>45 days</b>	<b>Mon 12/10/09</b>	<b>Fri 11/12/09</b>															
20	<input checked="" type="checkbox"/> Interface Kick Off Conf. Call	1 day	Mon 12/10/09	Mon 12/10/09															
21	<input checked="" type="checkbox"/> Receive Meditech Specs	1 day	Mon 12/10/09	Mon 12/10/09															
22	<input checked="" type="checkbox"/> Omnicell Delivery of Interfaces	1 day	Mon 19/10/09	Mon 19/10/09	20,21														
23	<input checked="" type="checkbox"/> Meditech Delivery of Interface Package	1 day	Mon 07/12/09	Mon 07/12/09															
24	<input checked="" type="checkbox"/> Conference call - Testing discussion	4 days	Tue 08/12/09	Fri 11/12/09	23														
25	<input checked="" type="checkbox"/> <b>Interface Testing</b>	<b>106 days</b>	<b>Tue 20/10/09</b>	<b>Tue 16/03/10</b>															
26	Establish ADT Connectivity	1 day	Tue 20/10/09	Tue 20/10/09	20,21,22														
27	<input checked="" type="checkbox"/> <b>Test ADT</b>	<b>4 days</b>	<b>Mon 16/11/09</b>	<b>Thu 19/11/09</b>	<b>26</b>														
28	<input checked="" type="checkbox"/> Testing Discussion & WebEx	1 day	Mon 16/11/09	Mon 16/11/09															
29	<input checked="" type="checkbox"/> Customer Testing	2 days	Tue 17/11/09	Wed 18/11/09															
30	<input checked="" type="checkbox"/> Testing Discussion	1 day	Thu 19/11/09	Thu 19/11/09	29														
31	<input checked="" type="checkbox"/> Interface Check Point Call	0 days	Wed 09/12/09	Wed 09/12/09															












Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	ep '09							20 Sep '09						
						M	T	W	T	F	S	S	M	T	W				
32	Establish RXC/ZPM Connectivity	1 day	Mon 14/12/09	Mon 14/12/09															
33	<b>Test RXC</b>	<b>4 days</b>	<b>Mon 14/12/09</b>	<b>Thu 17/12/09</b>															
34	Testing Discussion & WebEx	1 day	Mon 14/12/09	Mon 14/12/09															
35	Customer Testing	2 days	Tue 15/12/09	Wed 16/12/09															
36	Testing Discussion	1 day	Thu 17/12/09	Thu 17/12/09															
37	<b>Test ZPM</b>	<b>4 days</b>	<b>Mon 14/12/09</b>	<b>Thu 17/12/09</b>															
38	Testing Discussion & WebEx	1 day	Mon 14/12/09	Mon 14/12/09															
39	Customer Testing	2 days	Tue 15/12/09	Wed 16/12/09															
40	Testing Discussion	1 day	Thu 17/12/09	Thu 17/12/09															
41	Establish RXP/RXF Connectivity	1 day	Mon 04/01/10	Mon 04/01/10	22,20														
42	<b>Test RXP</b>	<b>4 days</b>	<b>Mon 11/01/10</b>	<b>Thu 14/01/10</b>															
43	Testing Discussion & WebEx	1 day	Mon 11/01/10	Mon 11/01/10															
44	Customer Testing	2 days	Tue 12/01/10	Wed 13/01/10	43														
45	Testing Discussion	1 day	Thu 14/01/10	Thu 14/01/10	44														
46	<b>Test RXF</b>	<b>4 days</b>	<b>Mon 11/01/10</b>	<b>Thu 14/01/10</b>															
47	Testing Discussion & WebEx	1 day	Mon 11/01/10	Mon 11/01/10															
48	Customer Testing	2 days	Tue 12/01/10	Wed 13/01/10															
49	Testing Discussion	1 day	Thu 14/01/10	Thu 14/01/10															
50	<b>Interface Move To Live</b>	<b>16 days</b>	<b>Tue 23/02/10</b>	<b>Tue 16/03/10</b>															
51	Request Live Port Info	15 days	Tue 23/02/10	Mon 15/03/10	33,37														
52	Establish Live connectivity	1 day	Mon 15/03/10	Mon 15/03/10															
53	Schedule Pre-seed	1 day	Mon 15/03/10	Mon 15/03/10															
54	Interface testing complete and live	1 day	Tue 16/03/10	Tue 16/03/10	27,33,52,37														
55	<b>Pharmacy Database/Cabinet Management</b>	<b>151 days</b>	<b>Wed 30/09/09</b>	<b>Wed 28/04/10</b>															
56	SMTP Email Set up	10 days	Mon 01/03/10	Fri 12/03/10	13														
57	Patient Type Aging	14 days	Mon 01/03/10	Thu 18/03/10	13														
58	Receive Master formulary - Excel	44 days	Wed 30/09/09	Mon 30/11/09															
59	Create OmniSuppliers	44 days	Mon 21/12/09	Thu 18/02/10	13														
60	Complete Patient Routing type	11 days	Mon 01/03/10	Mon 15/03/10	13														
61	Load Master onto Server	44 days	Mon 21/12/09	Thu 18/02/10	13														
62	Receive User List - Excel	44 days	Wed 30/09/09	Mon 30/11/09															

Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










ID	Task Name	Duration	Start	Finish	Predecessors	ep '09							20 Sep '09					
						M	T	W	T	F	S	S	M	T	W			
63	Load User Databases	44 days	Mon 21/12/09	Thu 18/02/10	13													
64	System admin to Add Pharm Staff	44 days	Fri 19/02/10	Wed 21/04/10	63													
65	Sizing tool Sent	44 days	Wed 30/09/09	Mon 30/11/09														
66	Receive Narc cassette / Dispenser list	1 day	Thu 25/02/10	Thu 25/02/10	65													
67	Order Narc cassette / Dispenser	44 days	Fri 26/02/10	Wed 28/04/10	66													
68	Obtain Static IP Addresses	8 days	Tue 23/02/10	Thu 04/03/10														
69	<b>Cabinet Deployment</b>	<b>19 days</b>	<b>Wed 27/01/10</b>	<b>Mon 22/02/10</b>														
70	ED Delivery - Cabinet	1 day	Wed 27/01/10	Wed 27/01/10														
71	ED Delivery - Cabinet Accessories	1 day	Wed 27/01/10	Wed 27/01/10														
72	Cabinet Delivery - Batch Delivery	1 day	Mon 22/02/10	Mon 22/02/10														
73	<b>Pharmacy Training</b>	<b>8 days?</b>	<b>Tue 26/01/10</b>	<b>Thu 04/02/10</b>														
74	Pharmacy trained on Cabinet functions	7 days?	Wed 27/01/10	Thu 04/02/10														
75	Train Systems Admin on Server functions	2 days?	Tue 26/01/10	Wed 27/01/10														
76	<b>Nurse Training</b>	<b>29 days?</b>	<b>Mon 22/02/10</b>	<b>Thu 01/04/10</b>														
77	Deploy Training Cabinet to Training location	0 days	Mon 22/02/10	Mon 22/02/10														
78	Training Cabinet Prep work	0 days	Mon 22/02/10	Mon 22/02/10														
79	Train Nursing Super Users	8 days	Tue 23/02/10	Thu 04/03/10														
80	Train Remaining Nurses	24 days?	Mon 01/03/10	Thu 01/04/10														
81	<b>Omniceil National Field Meeting - OC Offsite</b>	<b>5 days</b>	<b>Mon 08/02/10</b>	<b>Fri 12/02/10</b>														
82	<b>Cabinet Prep</b>	<b>12 days</b>	<b>Wed 24/02/10</b>	<b>Thu 11/03/10</b>	<b>71,72</b>													
83	Configure UBC Settings	12 days	Wed 24/02/10	Thu 11/03/10														
84	Accessories Installed	10 days	Wed 24/02/10	Tue 09/03/10														
85	Cabinet stocking - Non Controls	4 days	Mon 08/03/10	Thu 11/03/10														
86	Final Site Check All Par Locations	1 day	Thu 11/03/10	Thu 11/03/10														
87	<b>Phase 1 - ED / OR / PACU / ENDO</b>	<b>21 days</b>	<b>Fri 12/03/10</b>	<b>Fri 09/04/10</b>	<b>86</b>													
88	<b>OR / PACU / ENDO</b>	<b>4 days</b>	<b>Mon 15/03/10</b>	<b>Thu 18/03/10</b>														
89	Med Room Cleaning	0 days	Tue 16/03/10	Tue 16/03/10														
90	Cabinet stocking - Controls	16 days	Fri 12/03/10	Fri 02/04/10														
91	Deploy to Unit	0 days	Tue 16/03/10	Tue 16/03/10														
92	Assign Fridge Meds	0 days	Tue 16/03/10	Tue 16/03/10	91													
93	Go-Live	0 days	Tue 16/03/10	Tue 16/03/10	92													


Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	ep '09							20 Sep '09						
						M	T	W	T	F	S	S	M	T	W				
94	Go-Live Support	3 days	Tue 16/03/10	Thu 18/03/10	93														
95	Cabinet stocking - Non Controls - next weeks cabinets	21 days	Fri 12/03/10	Fri 09/04/10															
96	<b>ED</b>	<b>4 days</b>	<b>Mon 22/03/10</b>	<b>Thu 25/03/10</b>															
97	Med Room Cleaning	1 day	Mon 22/03/10	Mon 22/03/10															
98	Cabinet stocking - Controls	0 days	Tue 23/03/10	Tue 23/03/10	97														
99	Deploy to Unit	0 days	Tue 23/03/10	Tue 23/03/10	98														
100	Assign Fridge Meds	0 days	Tue 23/03/10	Tue 23/03/10	99														
101	Go-Live	0 days	Tue 23/03/10	Tue 23/03/10	100														
102	Go-Live Support	3 days	Tue 23/03/10	Thu 25/03/10	101														
103	Cabinet stocking - Non Controls - next weeks cabinets	4 days	Mon 22/03/10	Thu 25/03/10															
104	<b>Phase 2 - 3N / ICU / 4S 1, 2, &amp; 3 / 4E</b>	<b>11 days</b>	<b>Fri 26/03/10</b>	<b>Fri 09/04/10</b>	<b>103</b>														
105	<b>3N &amp; ICU</b>	<b>4 days</b>	<b>Mon 29/03/10</b>	<b>Thu 01/04/10</b>															
106	Med Room Cleaning	0 days	Tue 30/03/10	Tue 30/03/10															
107	Cabinet stocking - Controls	0 days	Tue 30/03/10	Tue 30/03/10															
108	Deploy to Unit	1 day	Tue 30/03/10	Tue 30/03/10															
109	Assign Fridge Meds	0 days	Tue 30/03/10	Tue 30/03/10															
110	Go-Live	0 days	Tue 30/03/10	Tue 30/03/10	109														
111	Go-Live Support	2 days	Wed 31/03/10	Thu 01/04/10	110														
112	Cabinet stocking - Non Controls - next weeks cabinets	6 days	Fri 26/03/10	Fri 02/04/10															
113	<b>4S 1, 2, &amp; 3 / 4E</b>	<b>4 days</b>	<b>Mon 05/04/10</b>	<b>Thu 08/04/10</b>															
114	Med Room Cleaning	0 days	Mon 05/04/10	Mon 05/04/10															
115	Cabinet stocking - Controls	0 days	Tue 06/04/10	Tue 06/04/10															
116	Deploy to Unit	0 days	Tue 06/04/10	Tue 06/04/10															
117	Assign Fridge Meds	0 days	Tue 06/04/10	Tue 06/04/10	116														
118	Go-Live	0 days	Tue 06/04/10	Tue 06/04/10	117														
119	Go-Live Support	2 days	Tue 06/04/10	Wed 07/04/10	118														
120	Cabinet stocking - Non Controls - next weeks cabinets	11 days	Fri 26/03/10	Fri 09/04/10															
121	<b>Phase 3 - MAT-CHILD / MENTAL HEALTH / AMB CARE</b>	<b>4 days</b>	<b>Mon 12/04/10</b>	<b>Thu 15/04/10</b>															
122	<b>MAT-CHILD / MENTAL HEALTH / AMB CARE</b>	<b>4 days</b>	<b>Mon 12/04/10</b>	<b>Thu 15/04/10</b>															
123	Med Room Cleaning	0 days	Mon 12/04/10	Mon 12/04/10															
124	Cabinet stocking - Controls	0 days	Tue 13/04/10	Tue 13/04/10															


Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	Predecessors	ep '09					20 Sep '09				
						M	T	W	T	F	S	S	M	T	W
125	Deploy to Unit	0 days	Tue 13/04/10	Tue 13/04/10											
126	Assign Fridge Meds	0 days	Tue 13/04/10	Tue 13/04/10											
127	Go-Live	0 days	Tue 13/04/10	Tue 13/04/10											
128	Go-Live Support	3 days	Tue 13/04/10	Thu 15/04/10	125										
129	<b>Phase 4 - SecureVault</b>	<b>4 days</b>	<b>Mon 19/04/10</b>	<b>Thu 22/04/10</b>											
130	<b>SecureVault Setup</b>	<b>9 days</b>	<b>Mon 12/04/10</b>	<b>Thu 22/04/10</b>											
131	Hardware Installation	2 days	Mon 12/04/10	Tue 13/04/10											
132	Training	3 days	Tue 20/04/10	Thu 22/04/10											
133	<b>SecureVault Installation</b>	<b>9 days</b>	<b>Mon 12/04/10</b>	<b>Thu 22/04/10</b>											
134	SecureVault Cabinet stocking	2 days	Mon 19/04/10	Tue 20/04/10											
135	Move Into Final Location	0 days	Tue 20/04/10	Tue 20/04/10											
136	Go-Live	0 days	Tue 20/04/10	Tue 20/04/10											
137	Go-Live Support	3 days	Tue 20/04/10	Thu 22/04/10											
138	<b>Exit Meeting / Clean Up</b>	<b>4 days</b>	<b>Mon 26/04/10</b>	<b>Thu 29/04/10</b>											
139	Go Live Support	4 days	Mon 26/04/10	Thu 29/04/10											
140	Site Clean Up	3 days	Mon 26/04/10	Wed 28/04/10											
141	System Admin Review	3 days	Mon 26/04/10	Wed 28/04/10											
142	Exit Meeting	0 days	Wed 28/04/10	Wed 28/04/10											




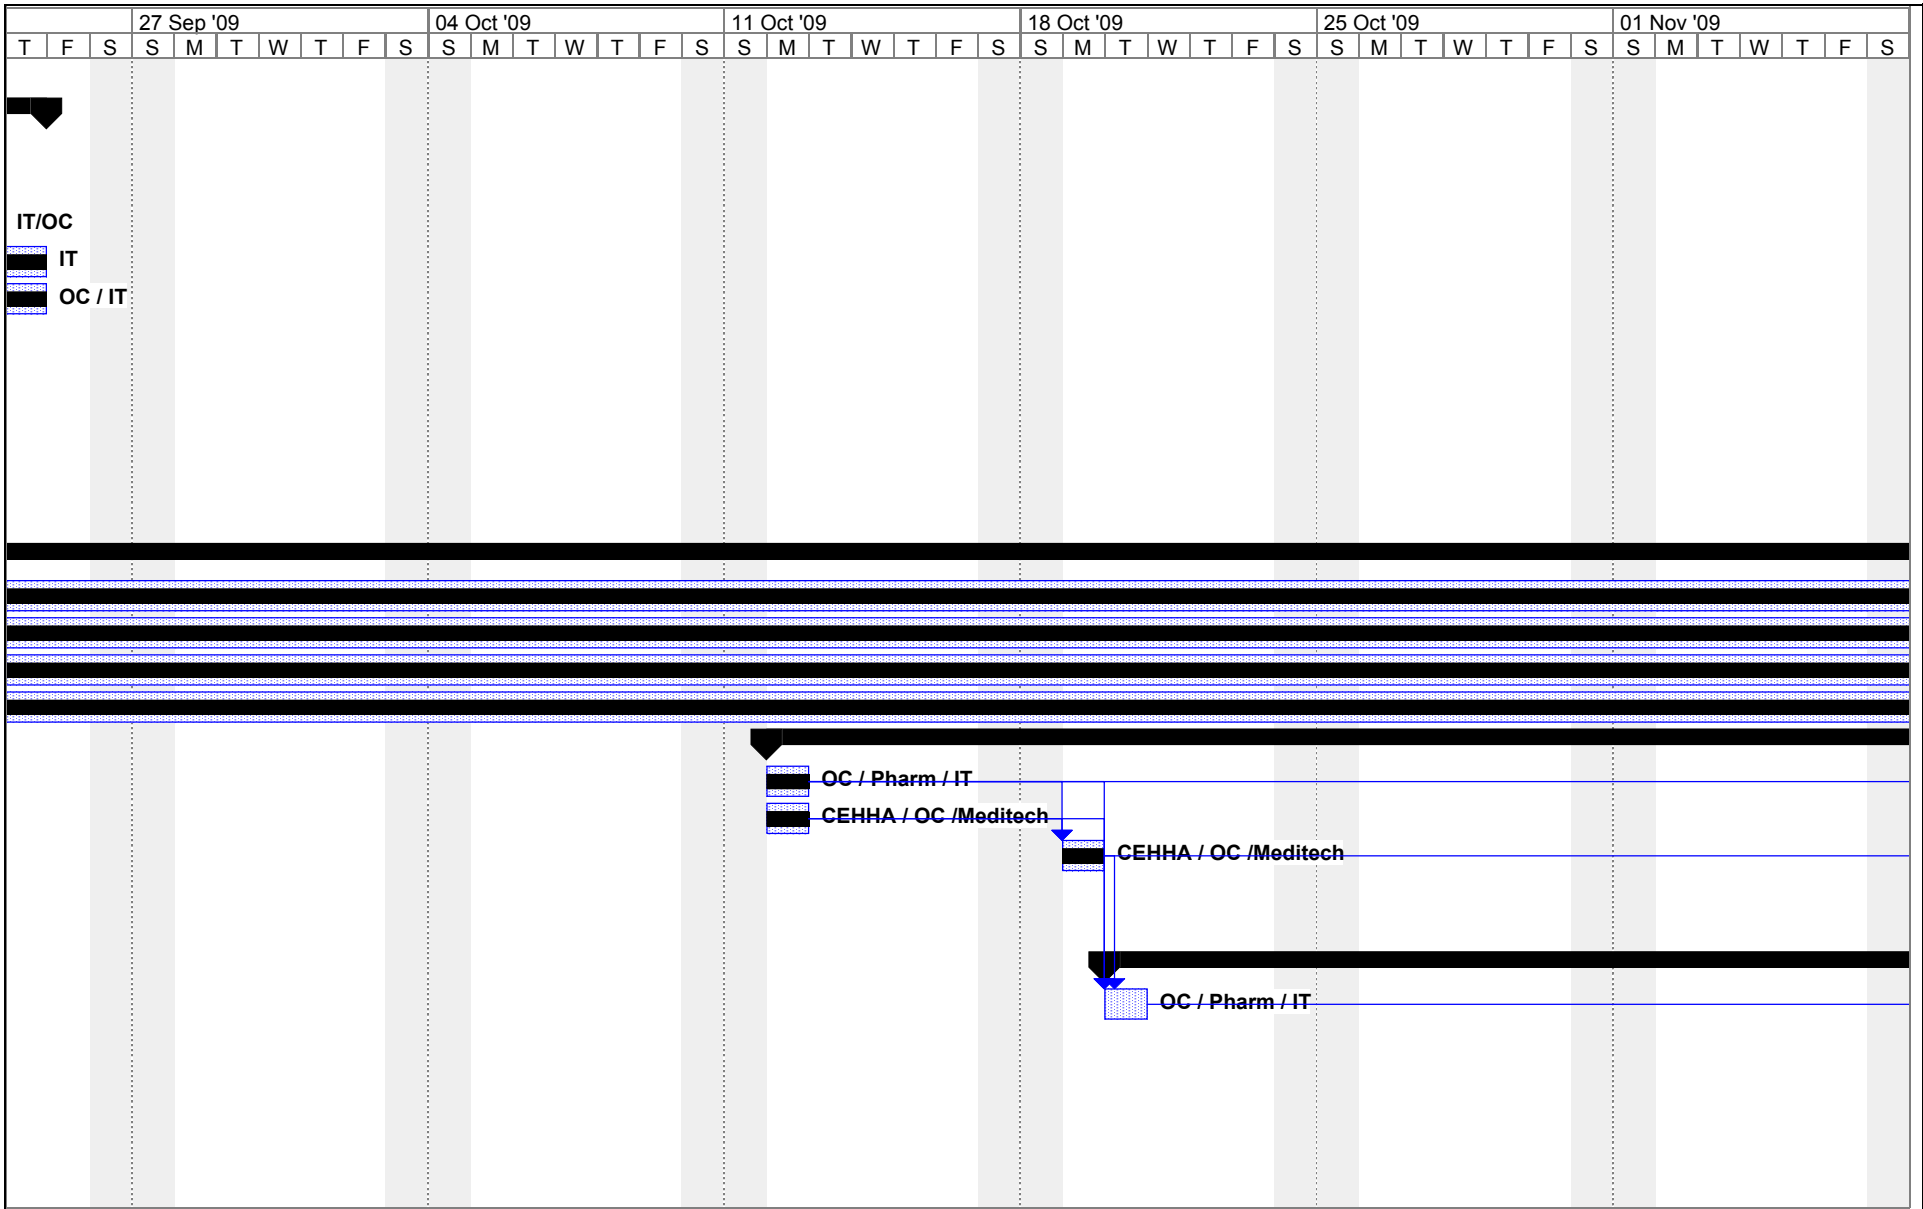



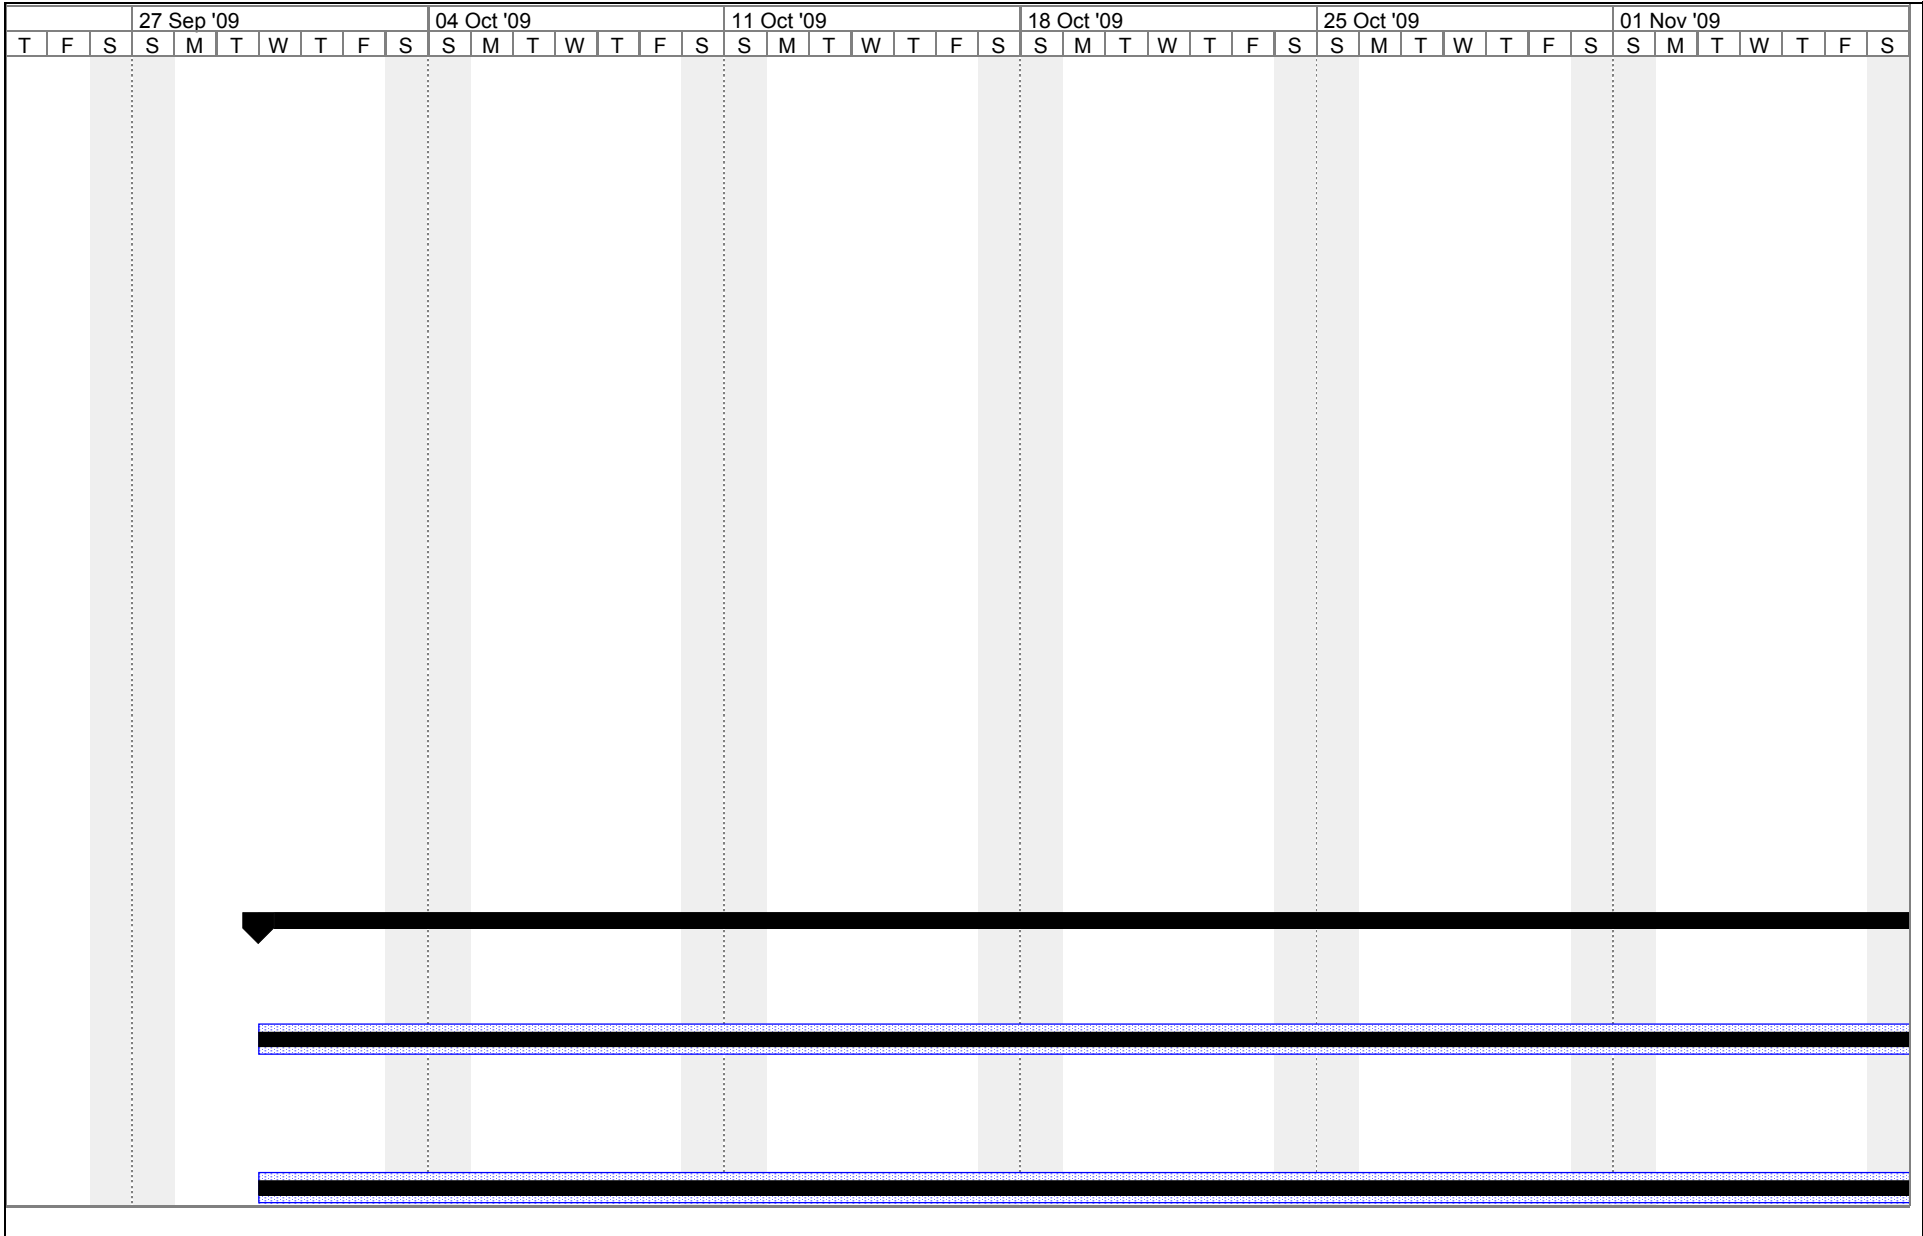

Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: Colchester  
Date: Fri 30/09/11








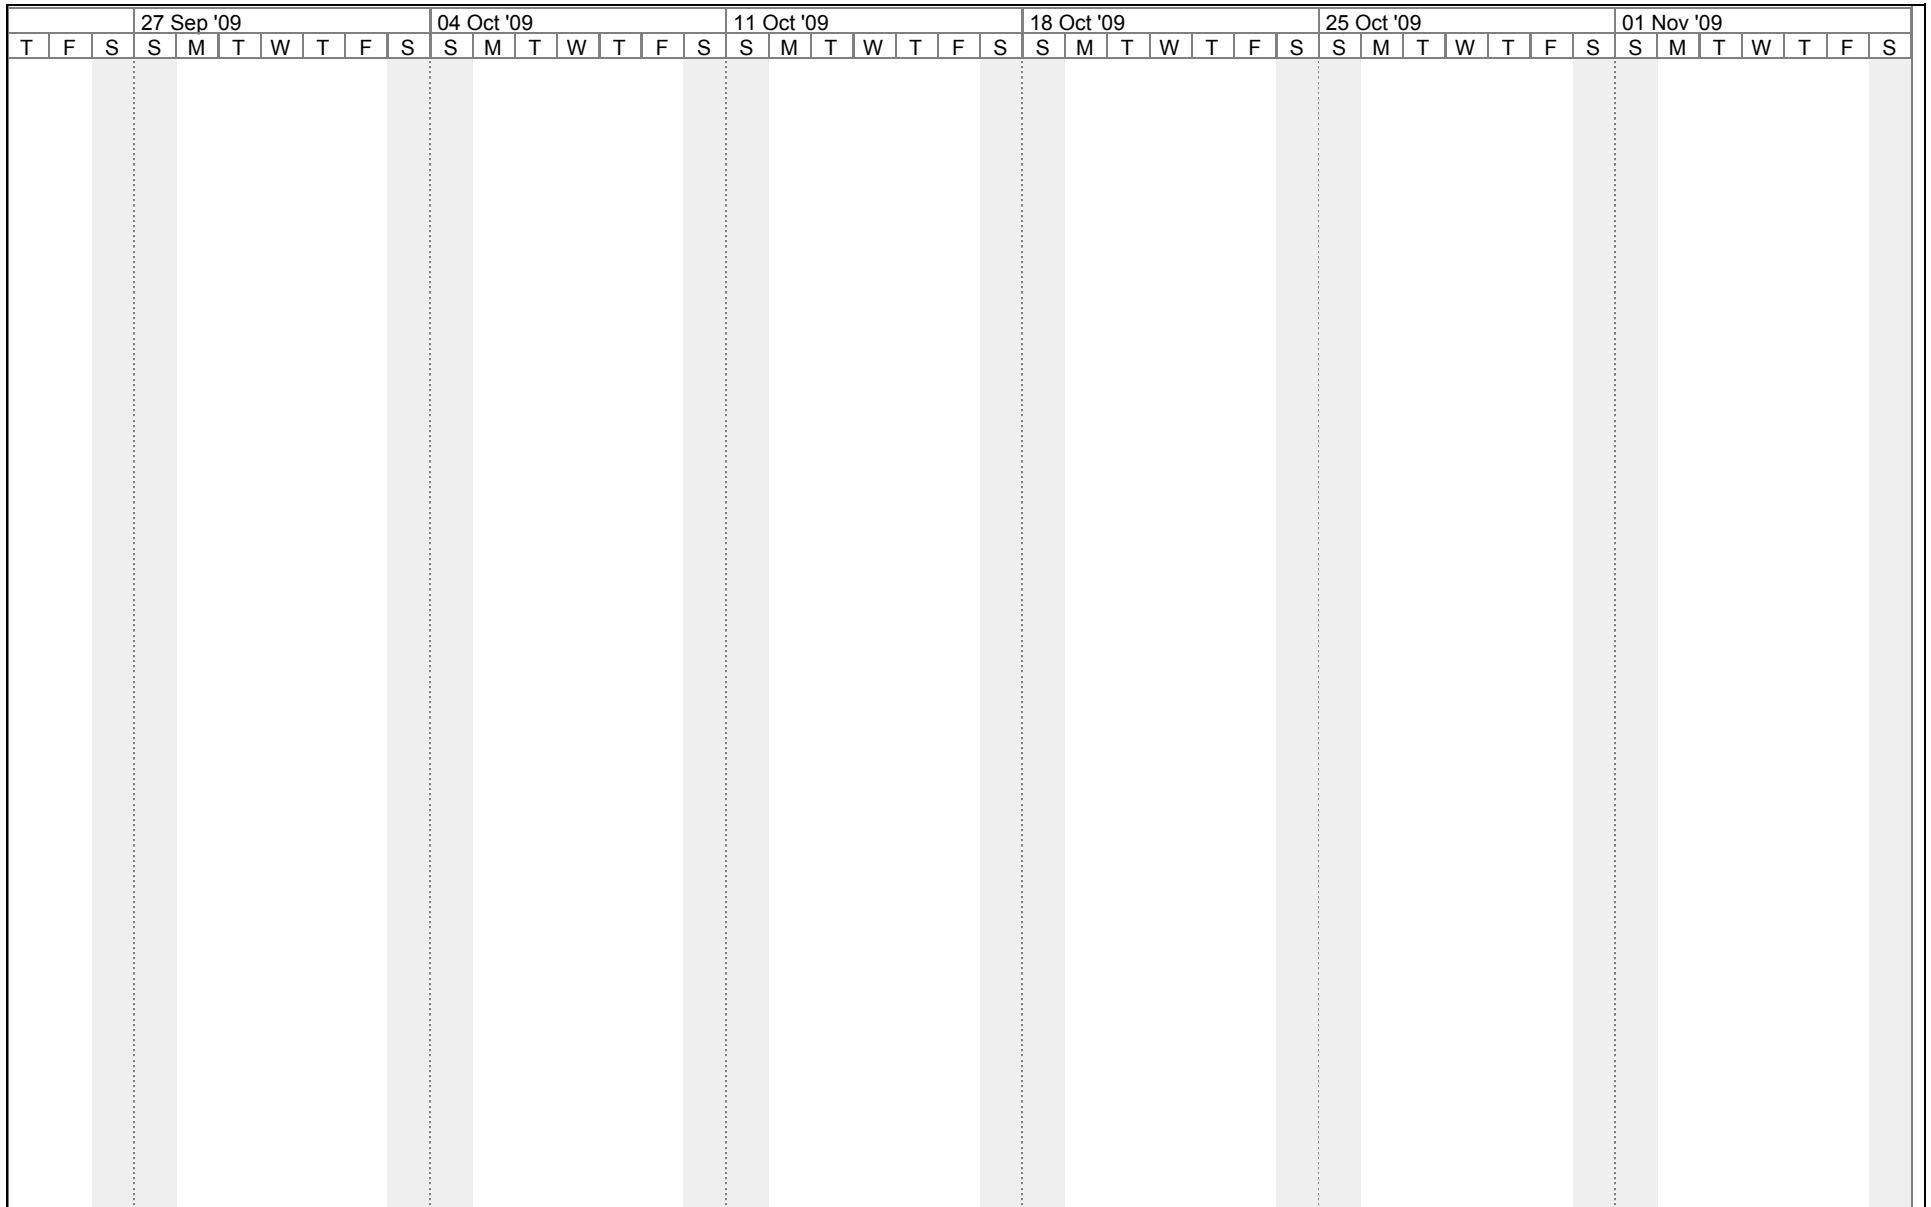

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	



Project: Colchester Date: Fri 30/09/11	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline















Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


27 Sep '09							04 Oct '09							11 Oct '09							18 Oct '09							25 Oct '09							01 Nov '09						
T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S				



Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

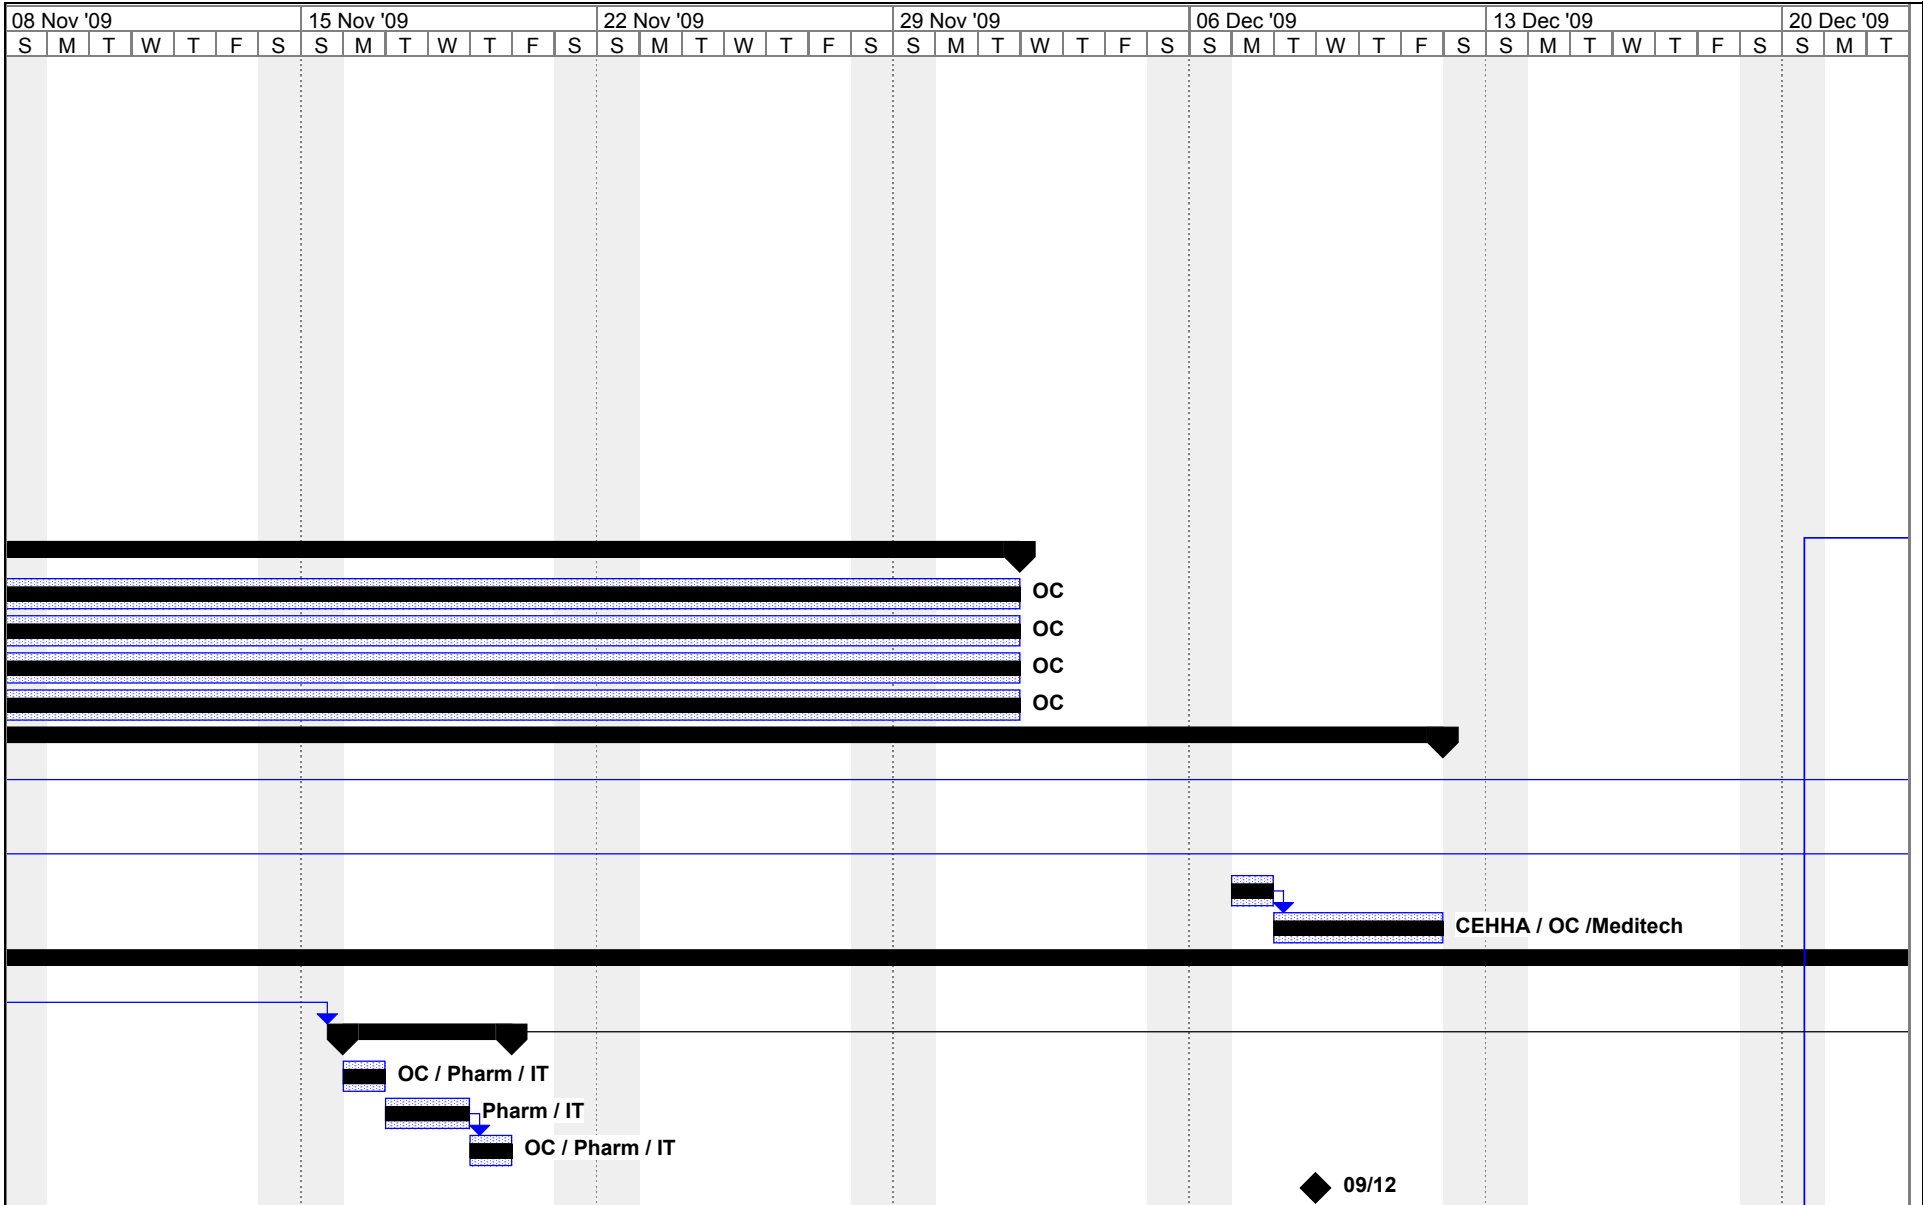




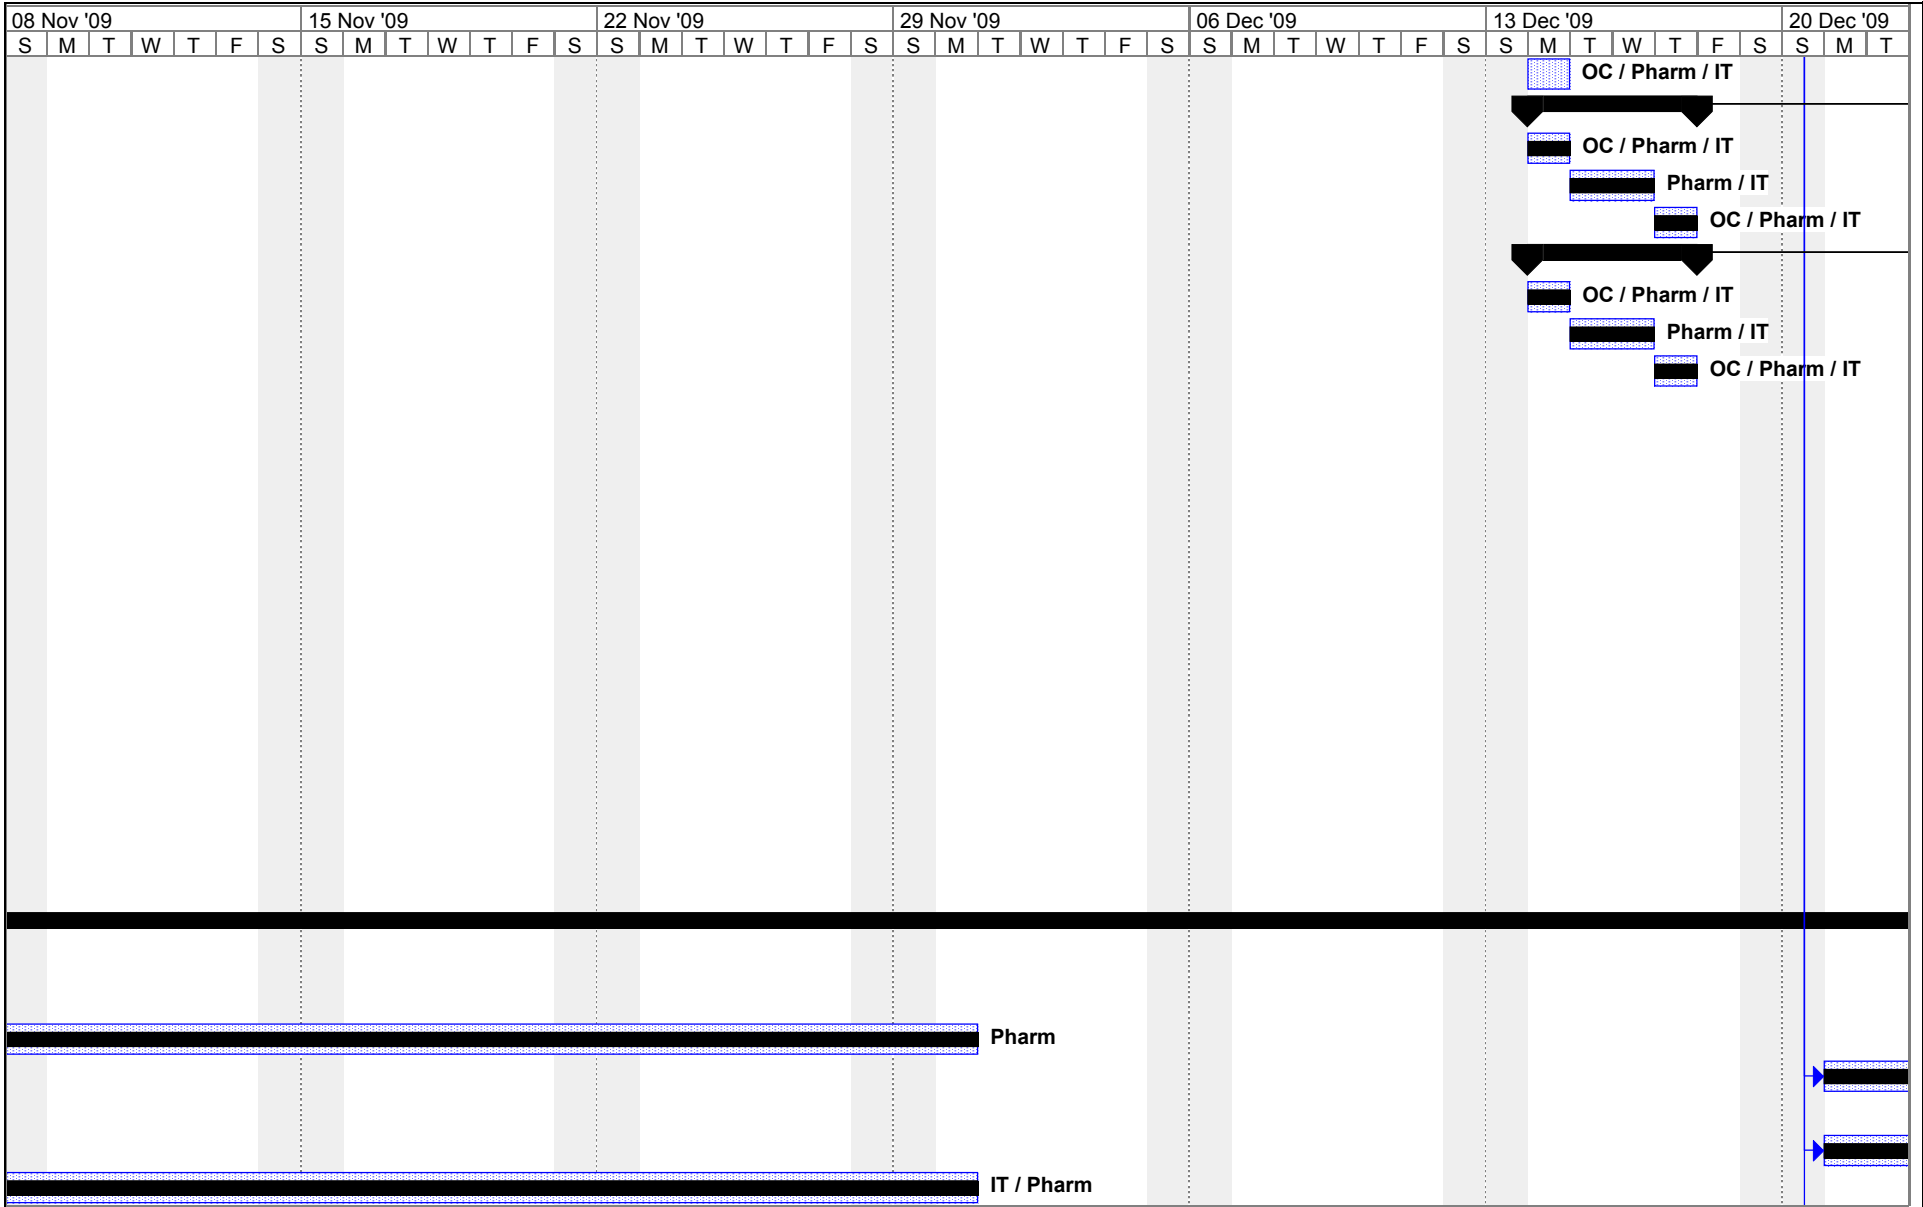





Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	













08 Nov '09							15 Nov '09							22 Nov '09							29 Nov '09							06 Dec '09							13 Dec '09							20 Dec '09		
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T

Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	


08 Nov '09							15 Nov '09							22 Nov '09							29 Nov '09							06 Dec '09							13 Dec '09							20 Dec '09		
S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T






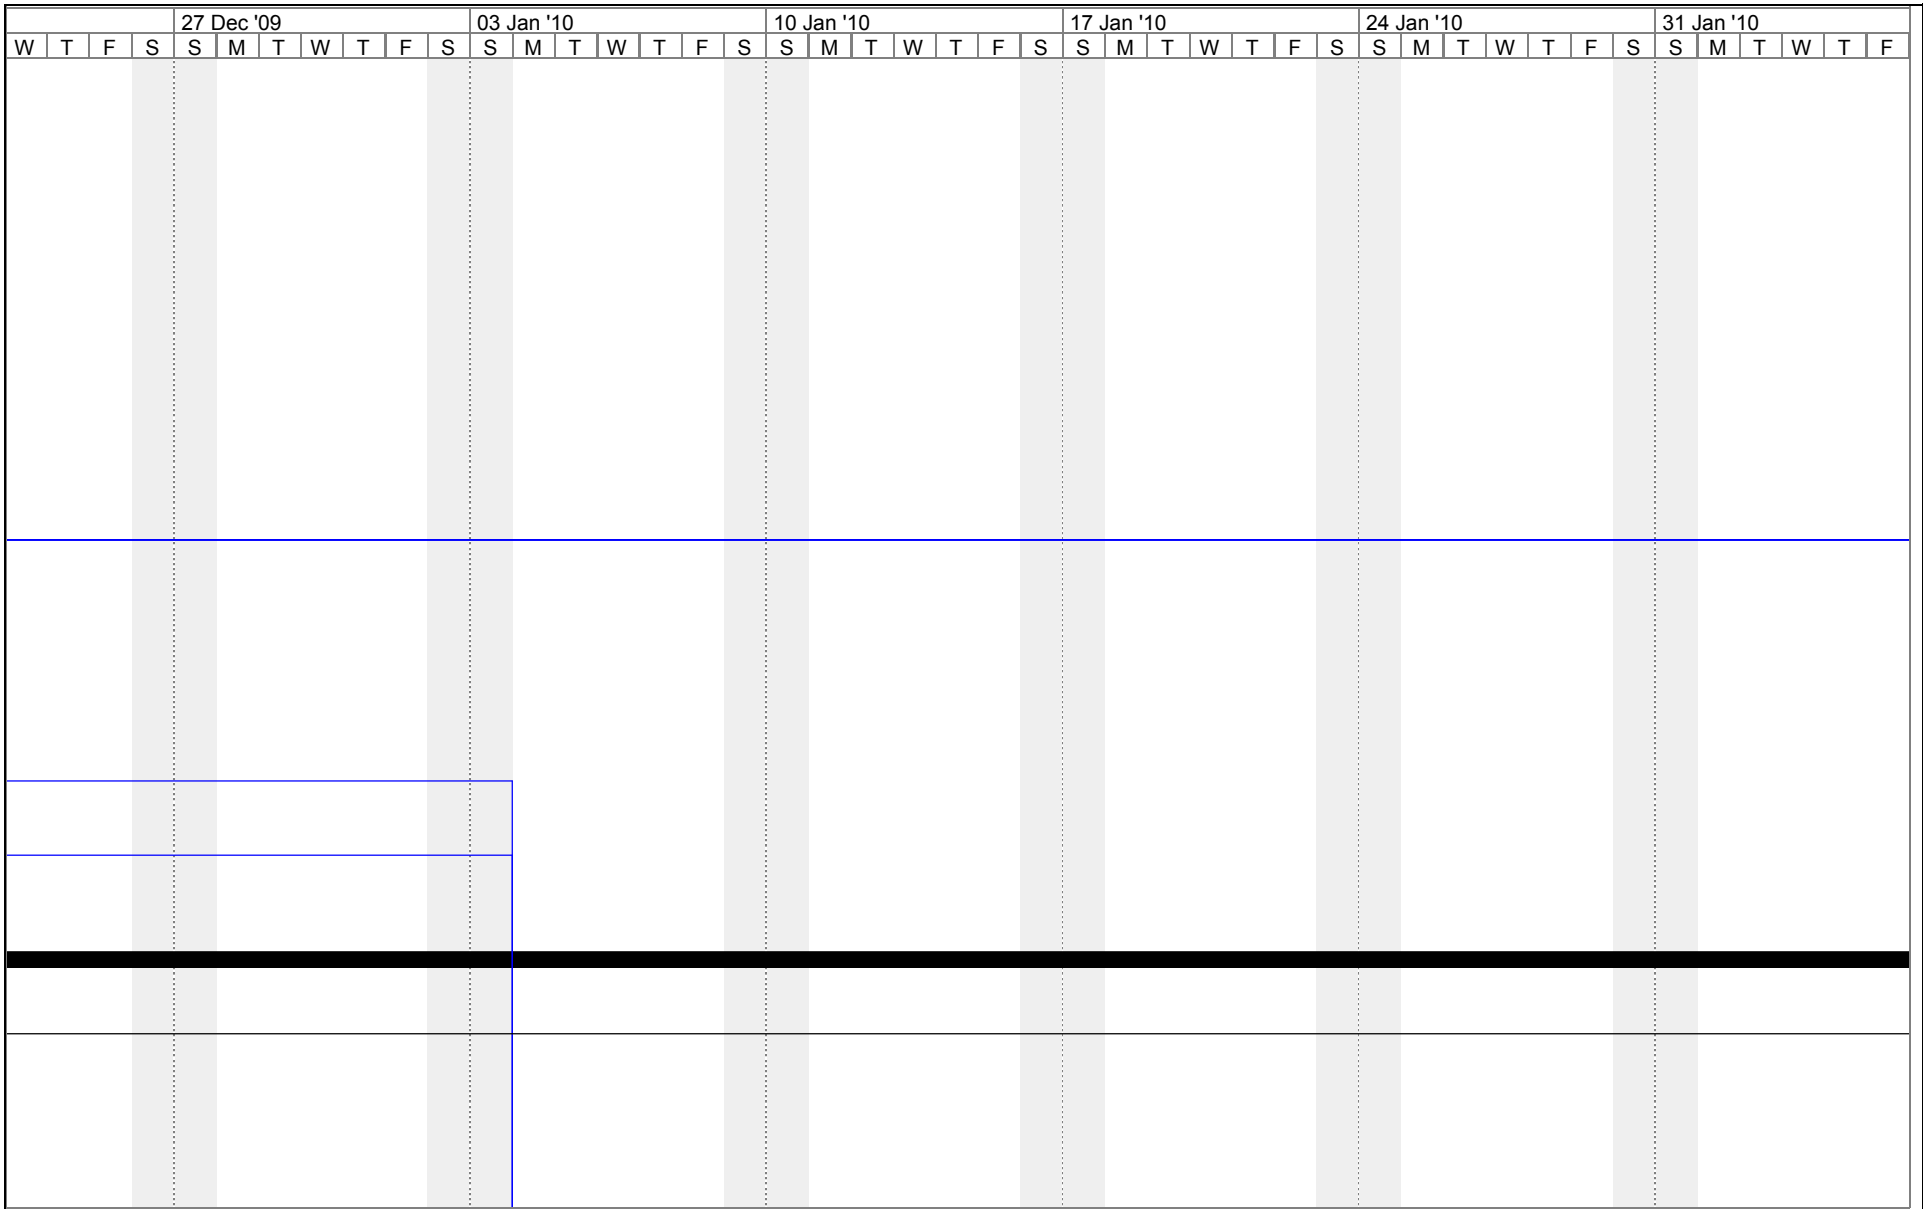



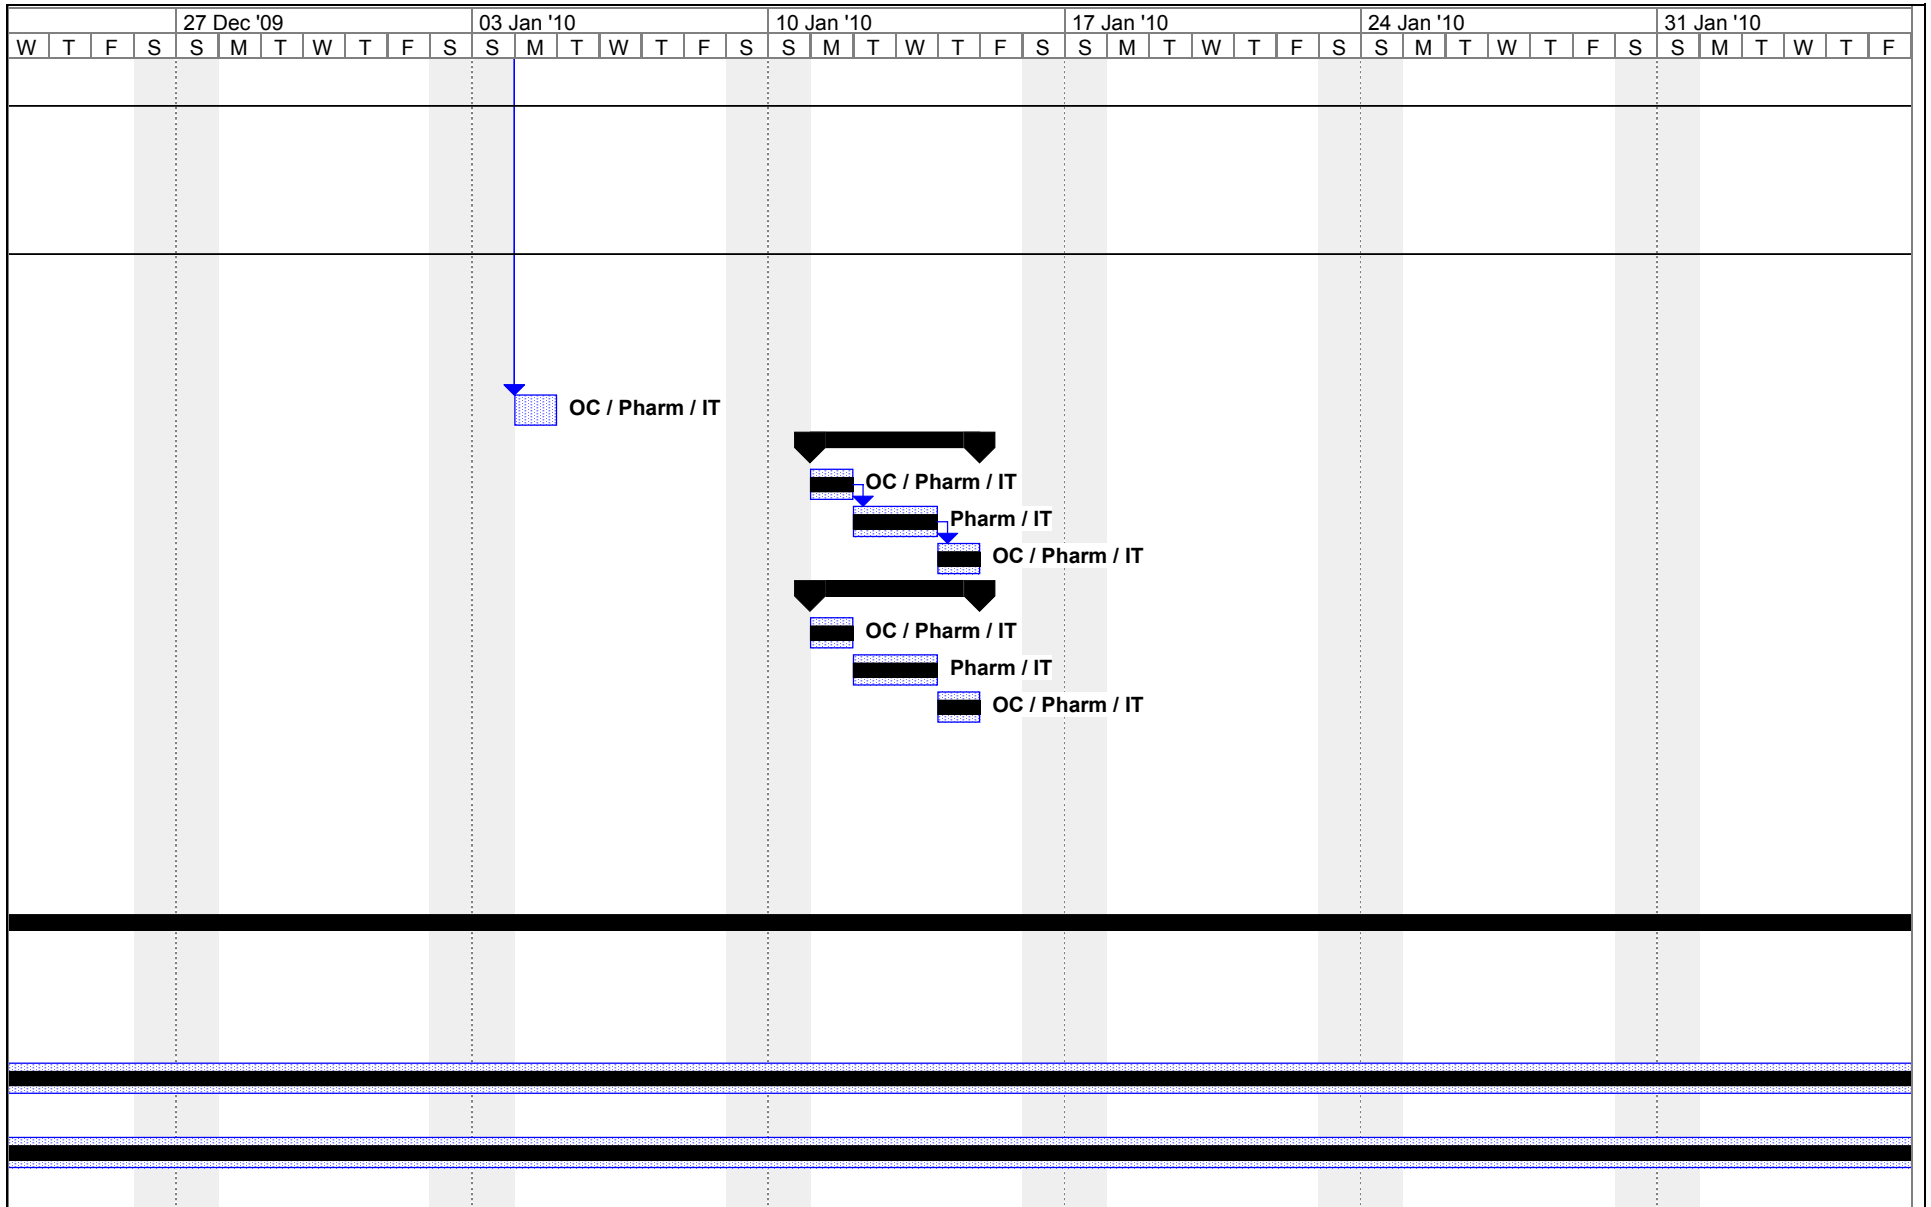


Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	










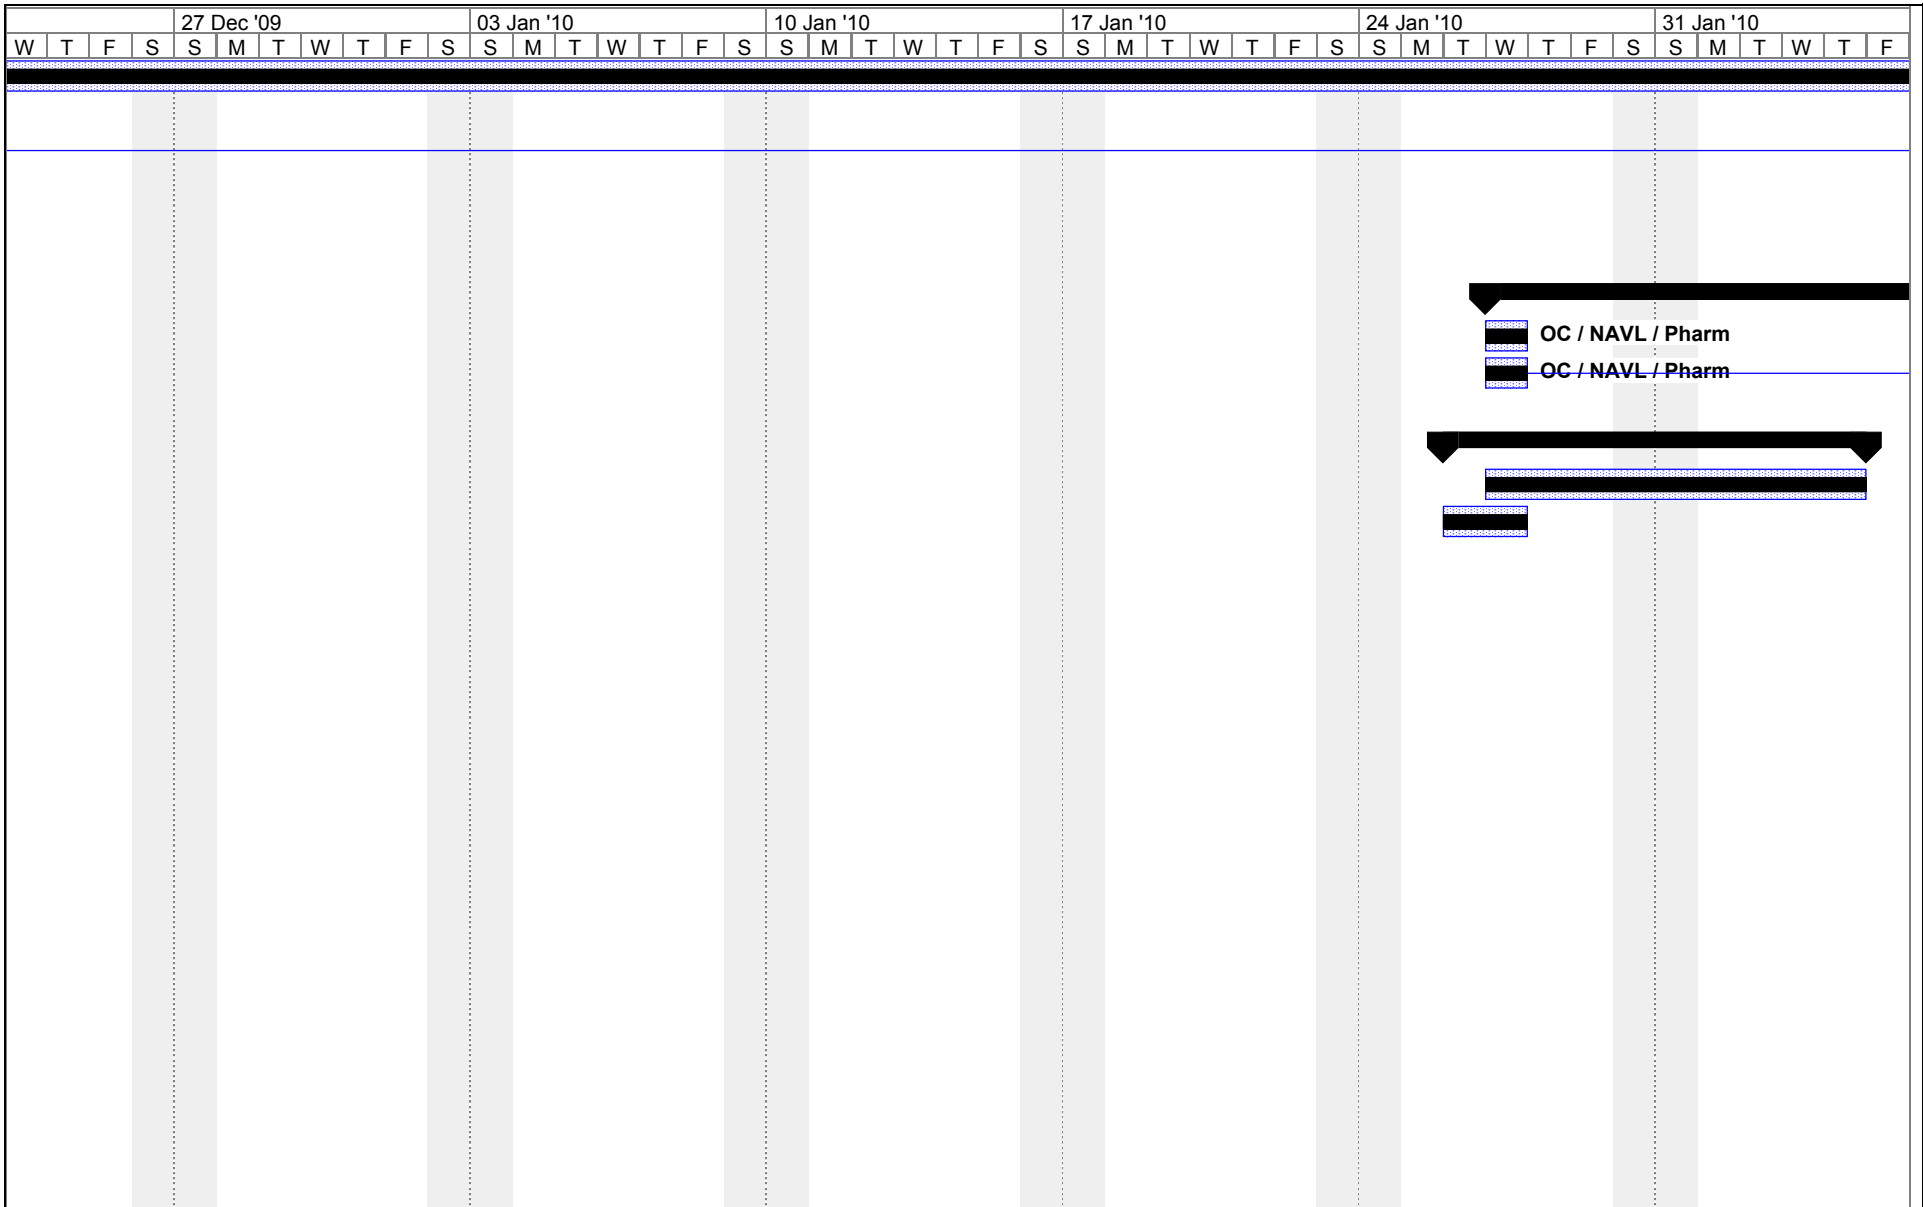














Project: Colchester Date: Fri 30/09/11	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 



Project: Colchester  
Date: Fri 30/09/11










Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	




Project: Colchester Date: Fri 30/09/11	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 





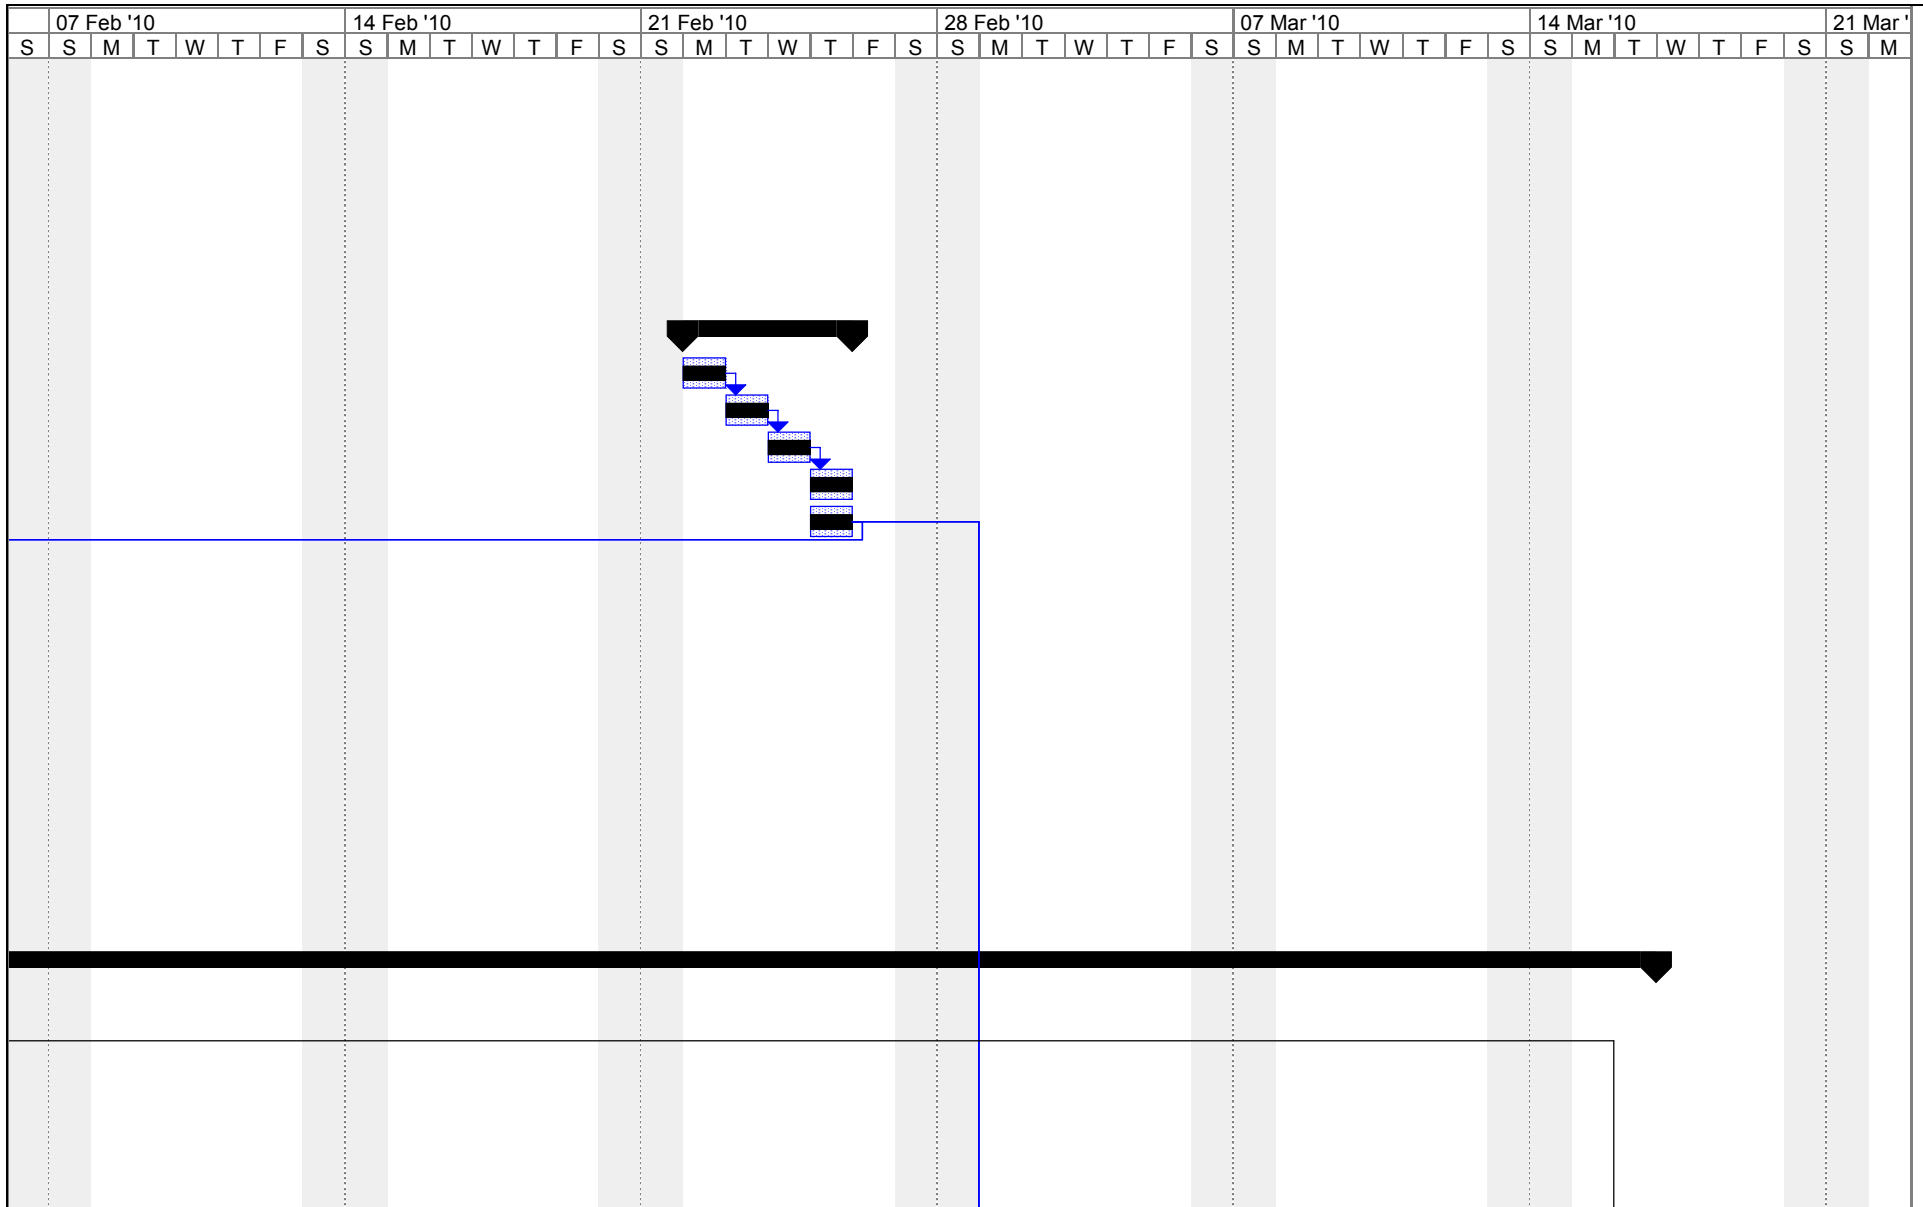

27 Dec '09				03 Jan '10				10 Jan '10				17 Jan '10				24 Jan '10				31 Jan '10															
W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S				




Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: Colchester  
Date: Fri 30/09/11


Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

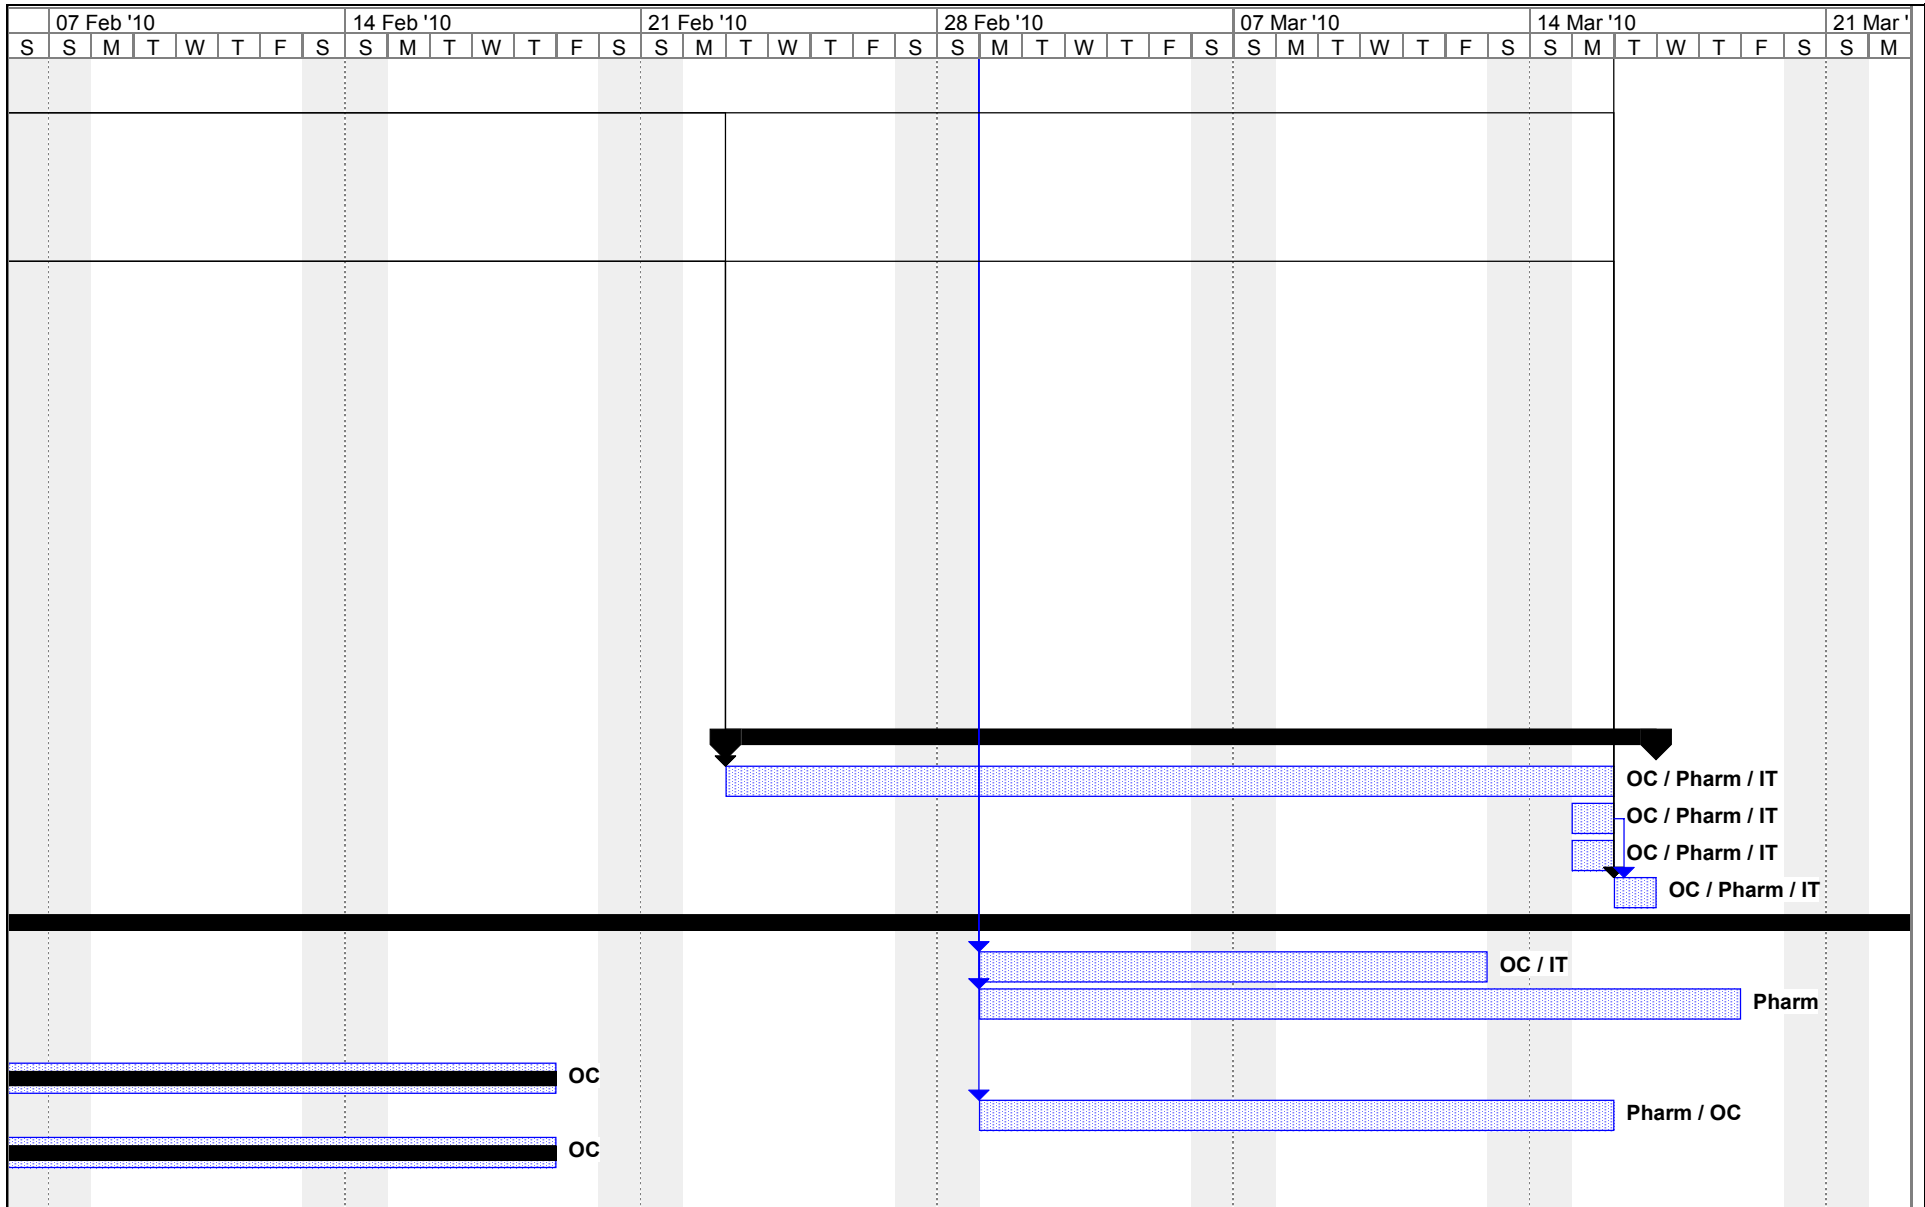

Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

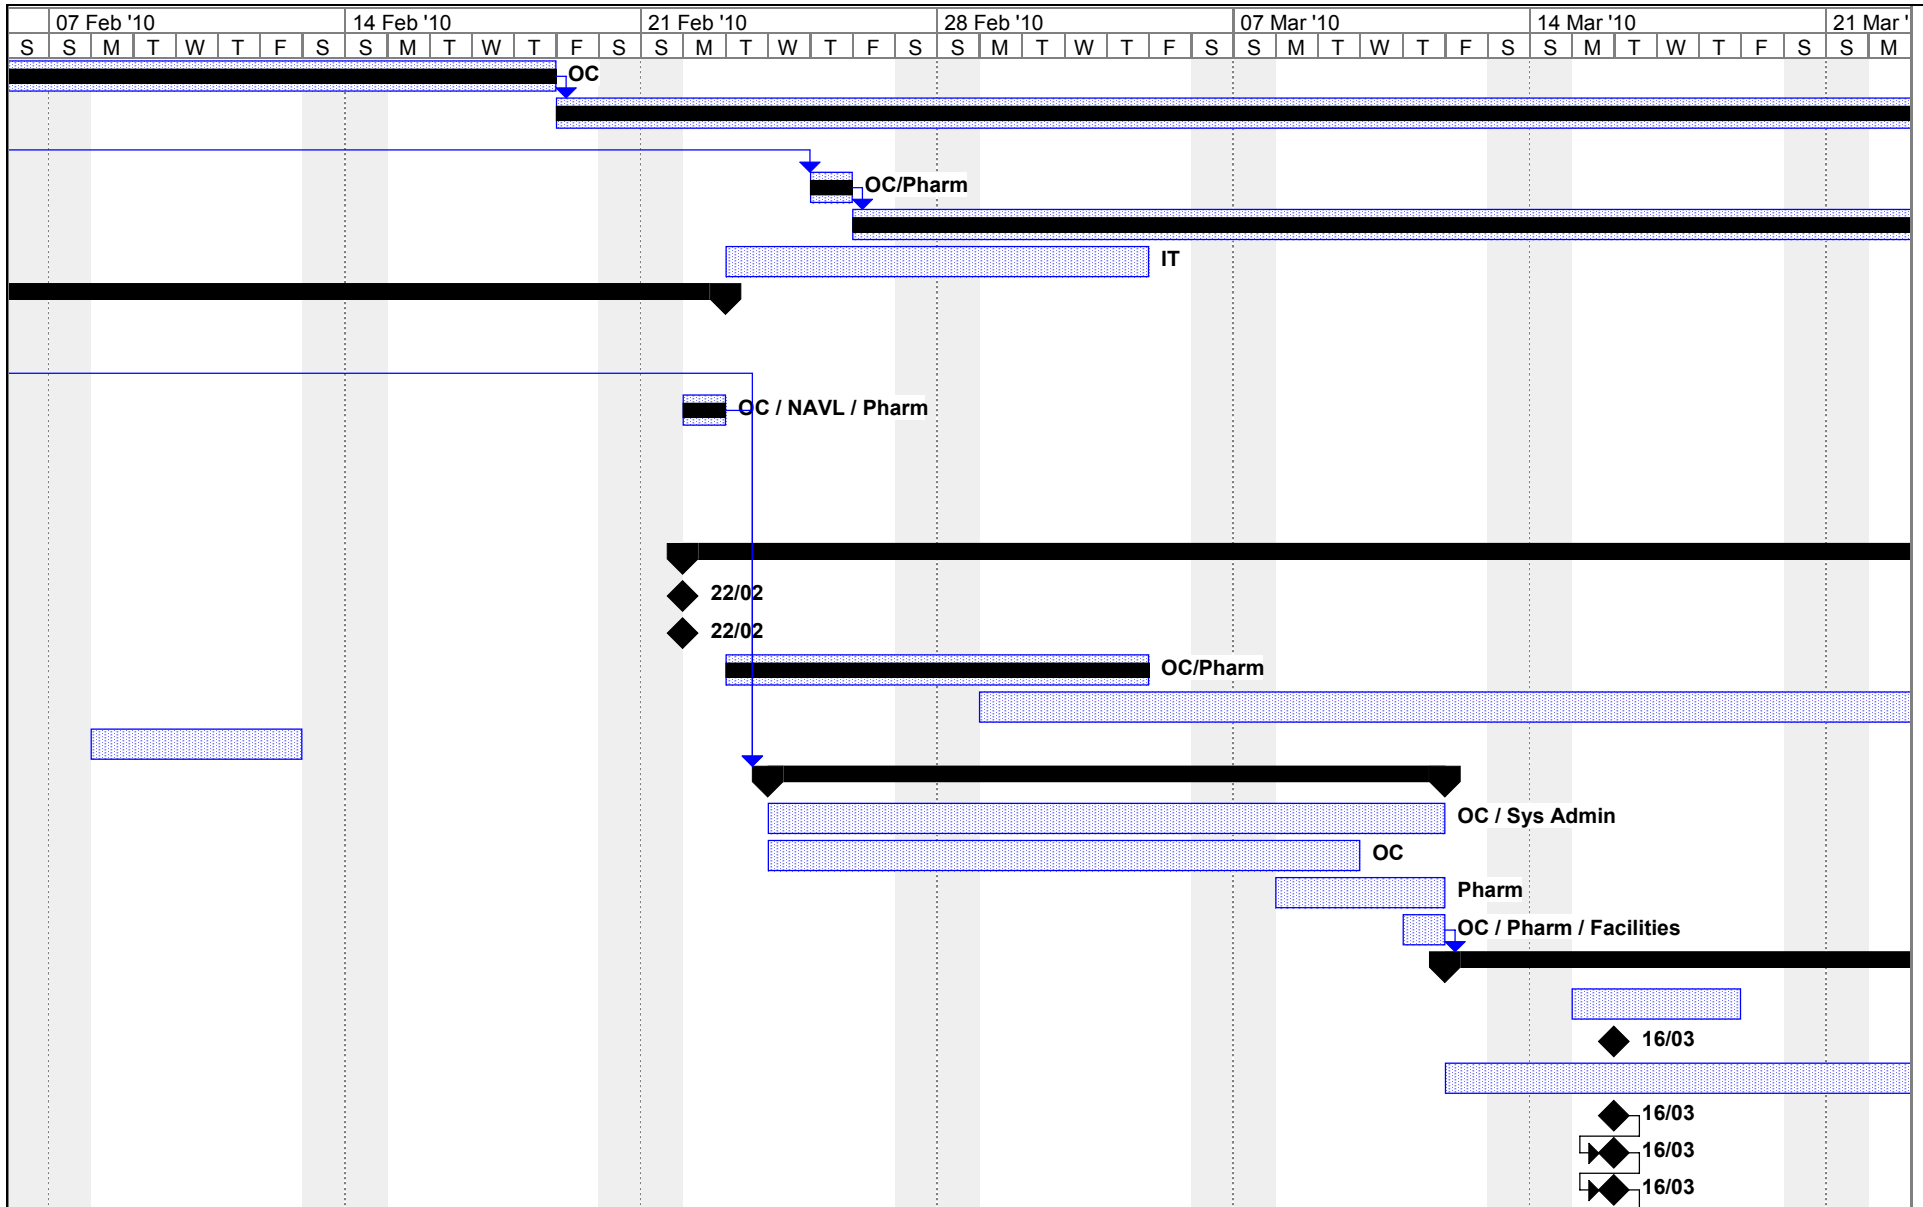

Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

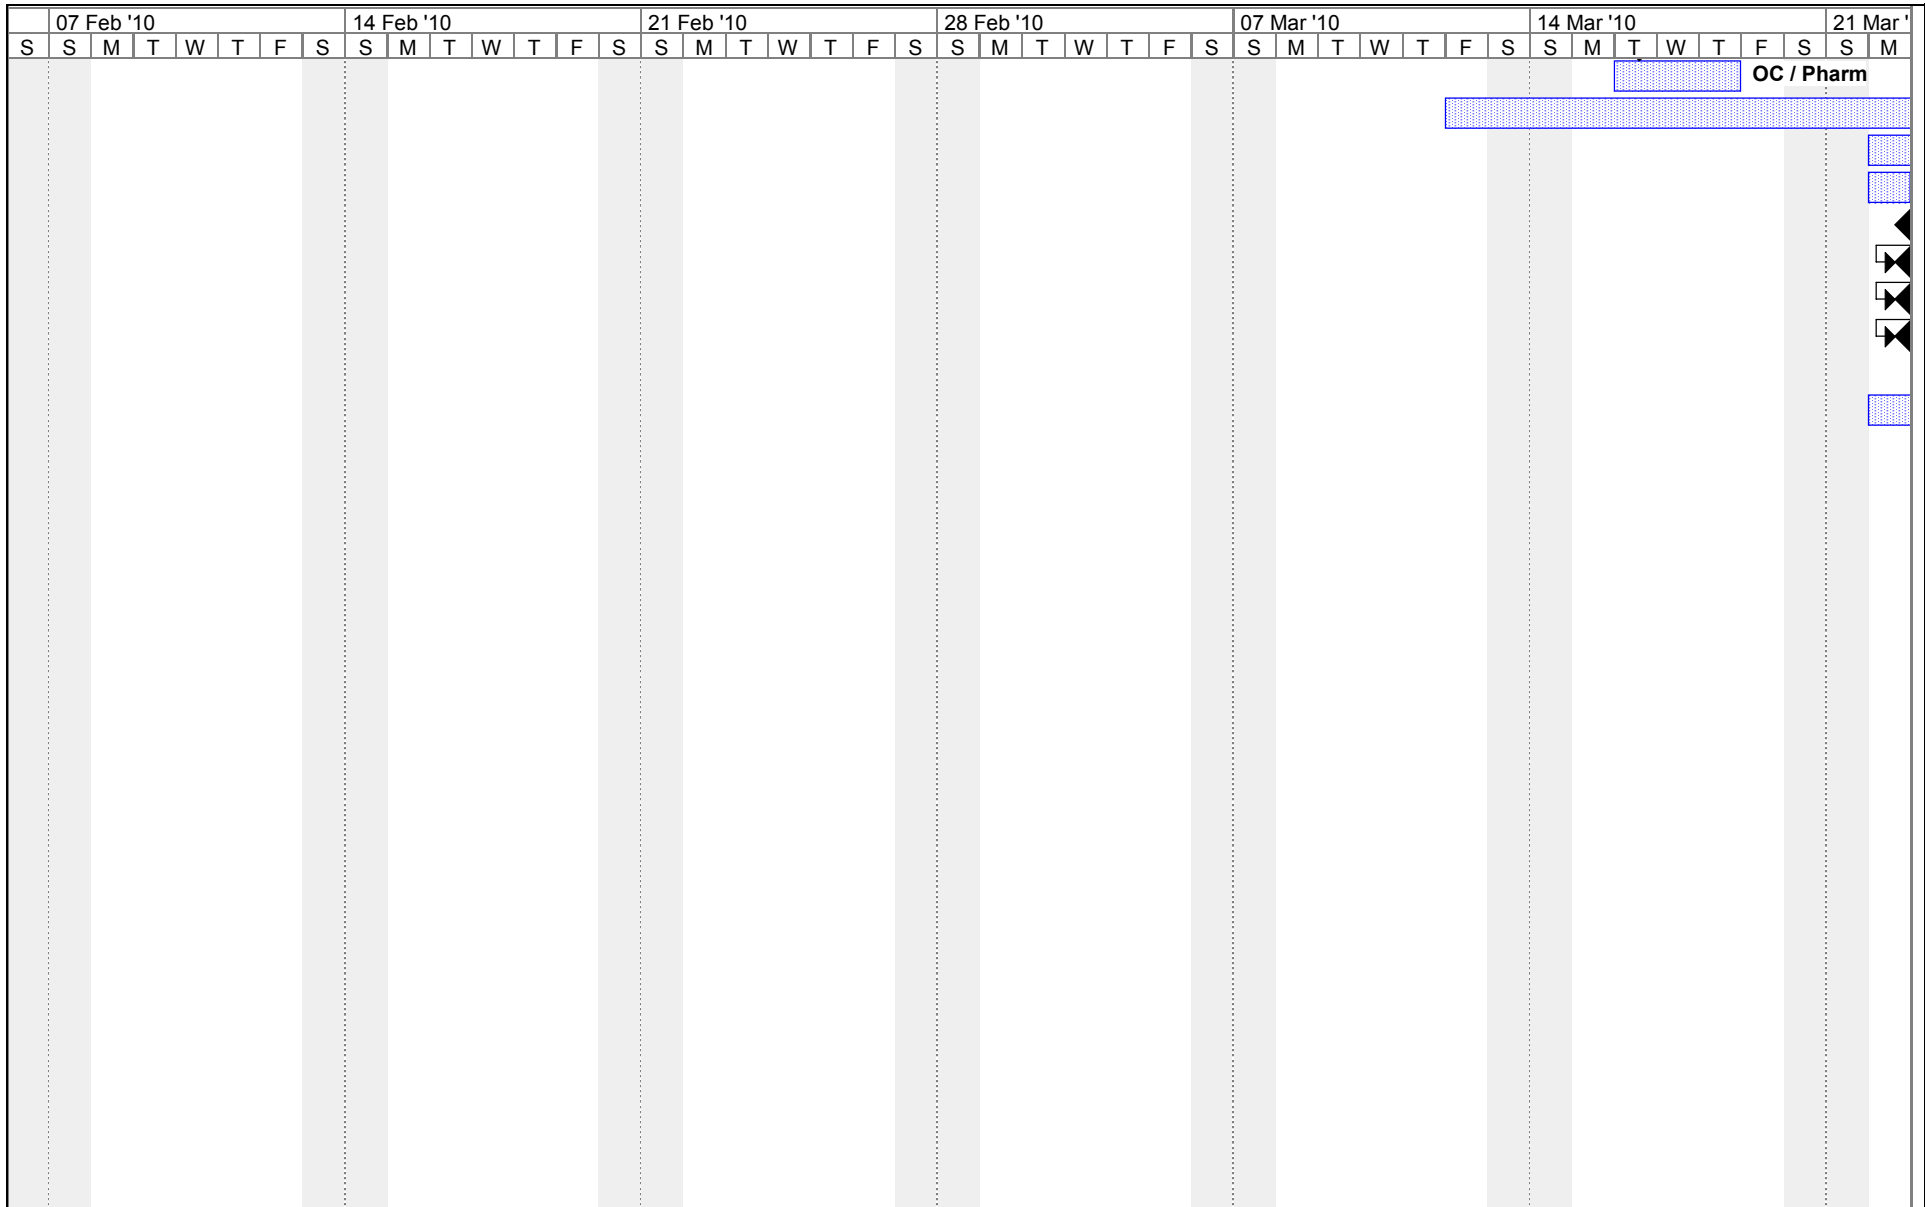










Project: Colchester Date: Fri 30/09/11	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline












07 Feb '10							14 Feb '10							21 Feb '10							28 Feb '10							07 Mar '10							14 Mar '10							21 Mar '10		
S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M




Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	




Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Colchester Date: Fri 30/09/11	Task	Milestone	External Tasks
	Split	Summary	External Milestone
	Progress	Project Summary	Deadline

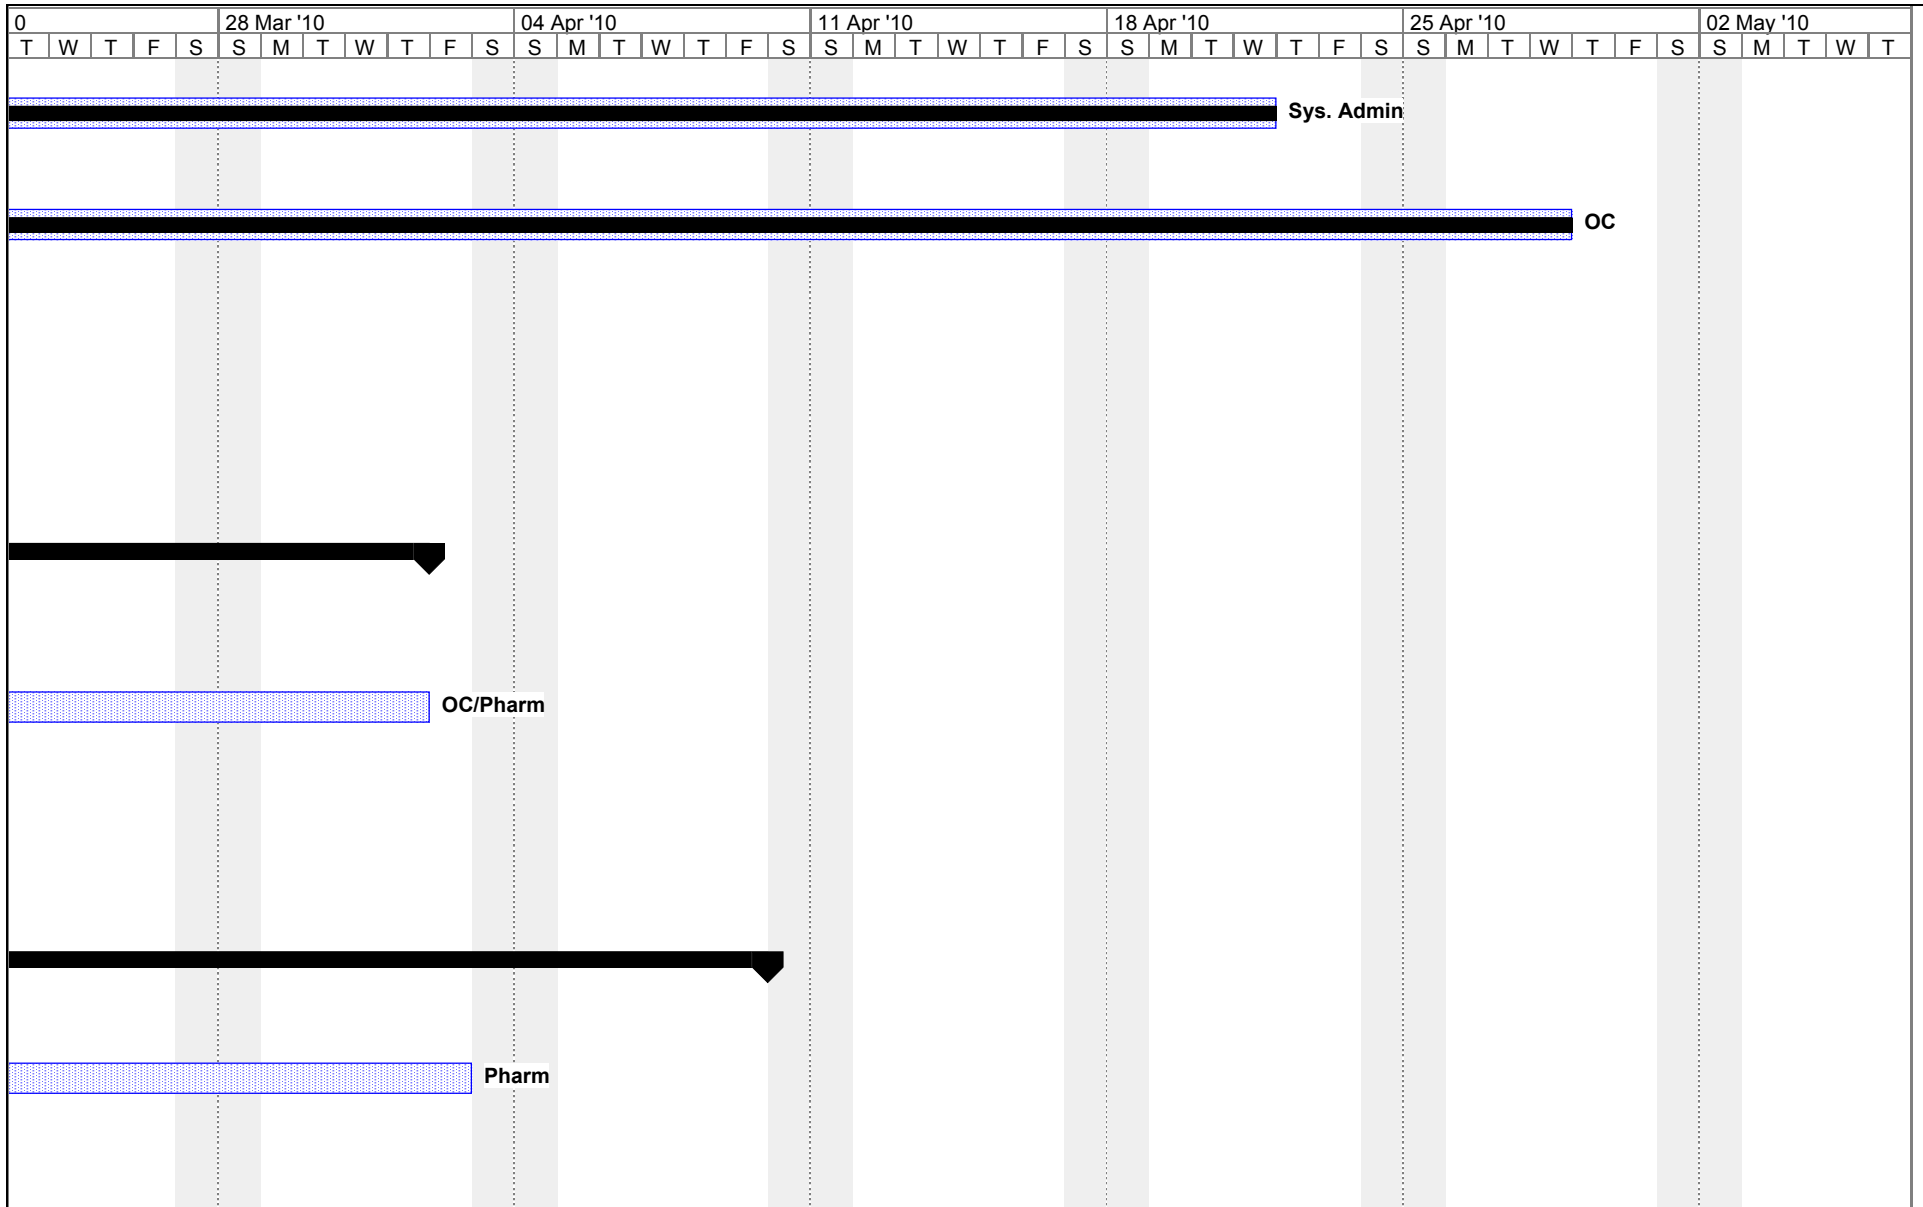


Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

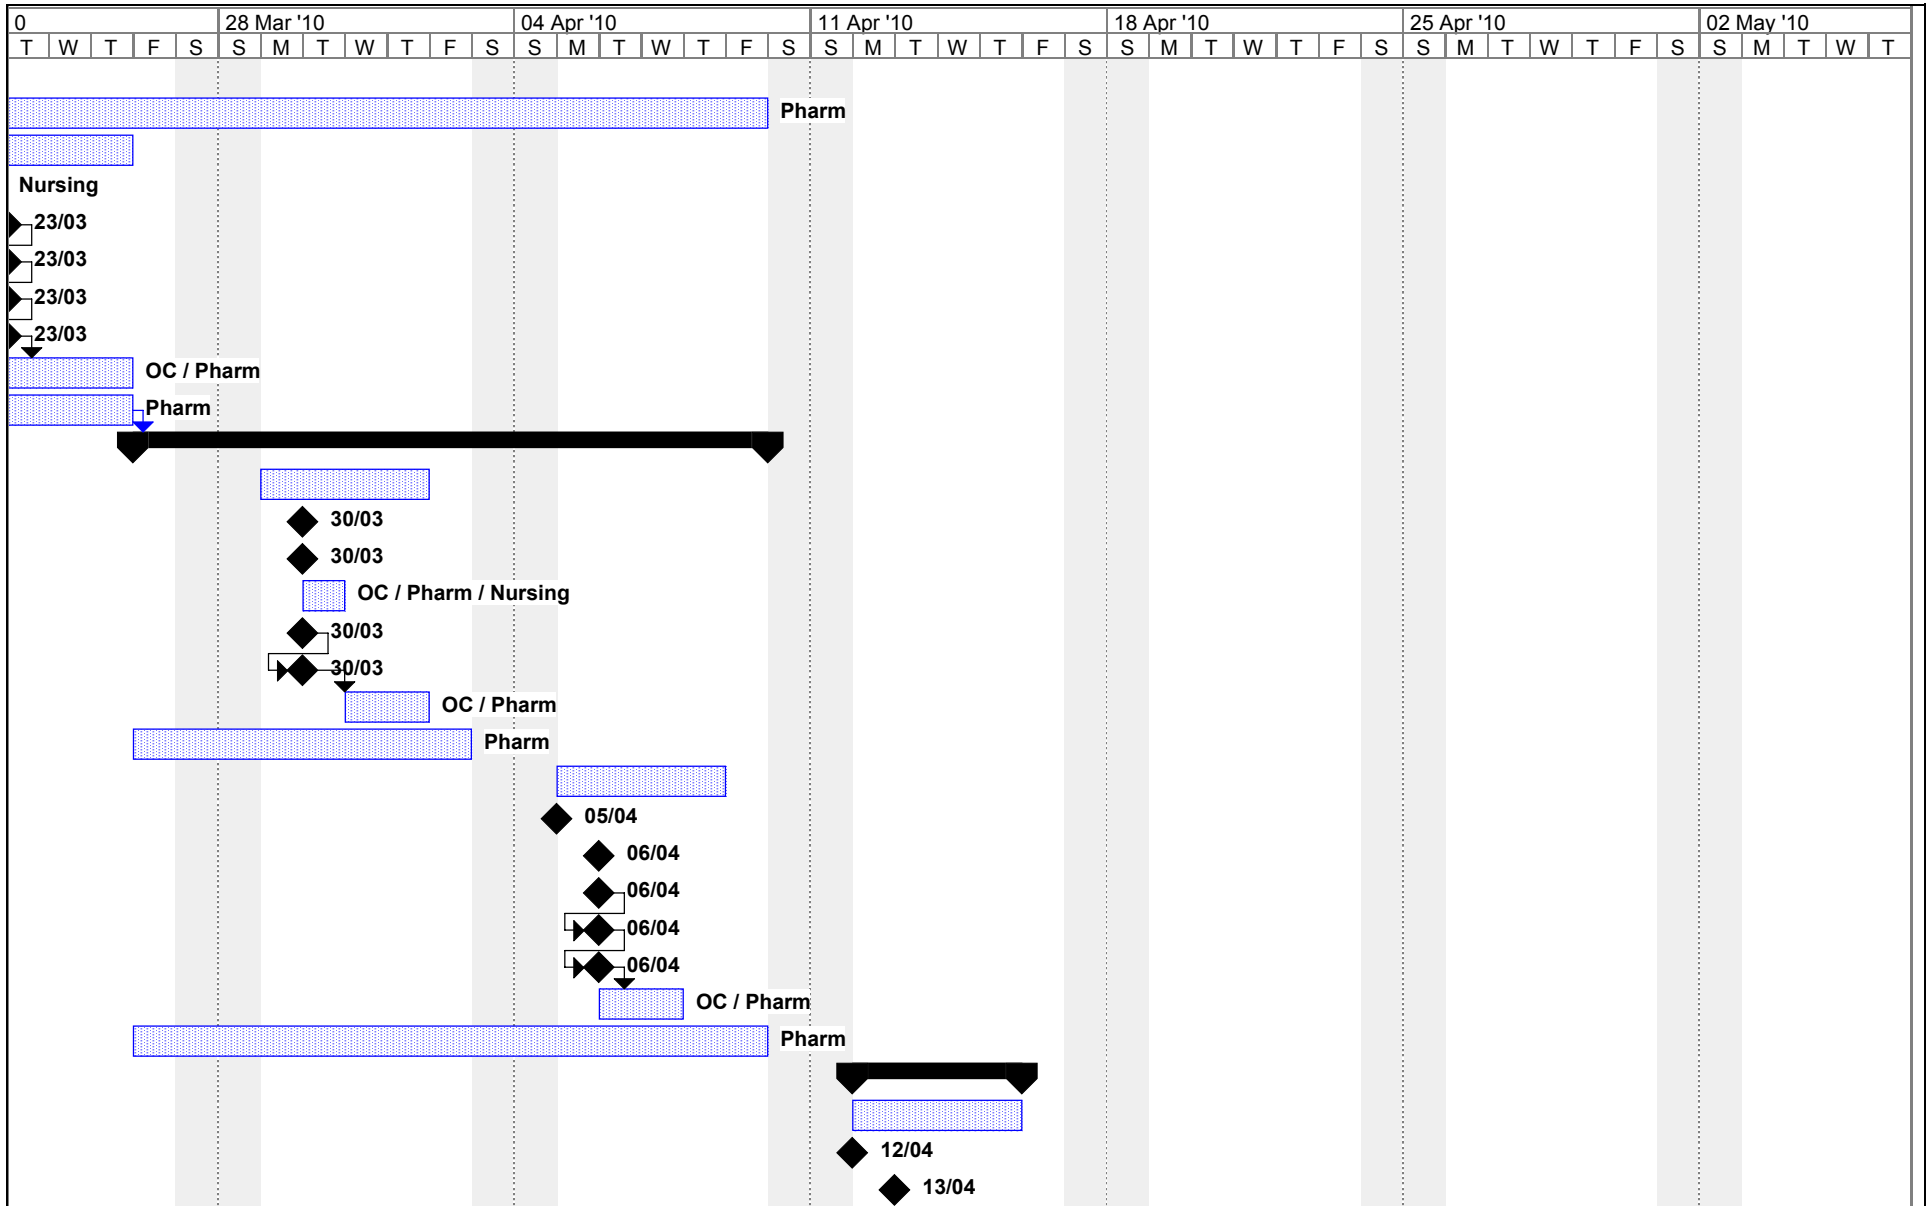

Project: Colchester  
Date: Fri 30/09/11

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	

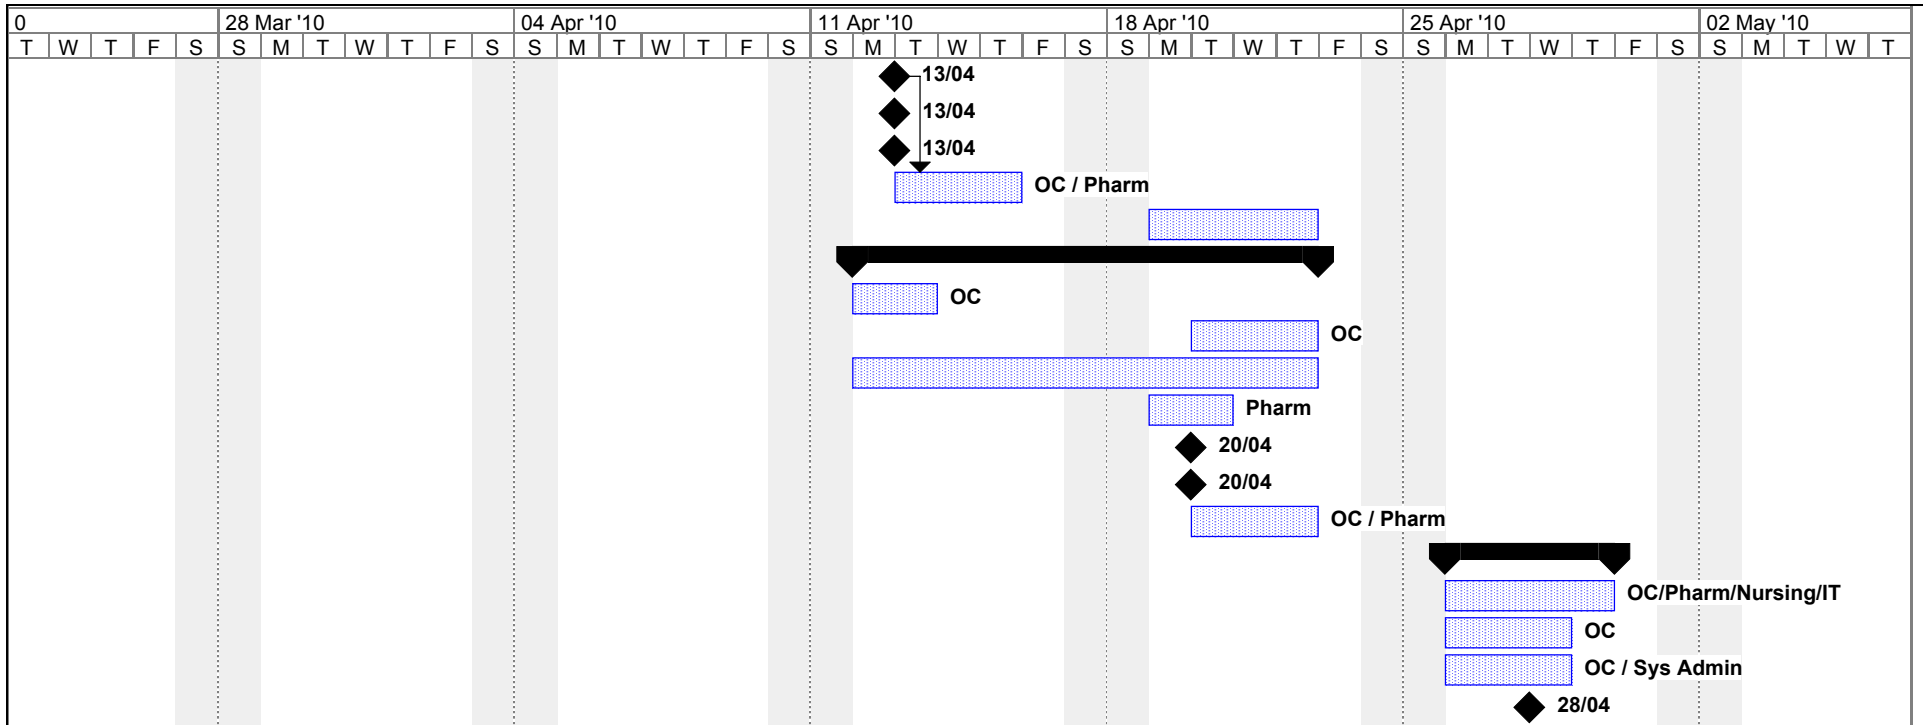

Project: Colchester Date: Fri 30/09/11	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
